

Enbridge Gas Inc.

50 Keil Drive N. Chatham, Ontario, Canada N7M 5M1

March 14, 2019

BY RESS & Courier

Ms. Kirsten Walli Board Secretary Ontario Energy Board Suite 2700, 2300 Yonge Street Toronto, Ontario M4P 1E4

Dear Ms. Walli:

Re: Enbridge Gas Inc. ("Enbridge Gas") Community Expansion Project Kettle and Stony Point First Nation and Lambton Shores Board File # EB-2015-0179

Pursuant to Condition 6 (b) i-v of the Board's Conditions of Approval for the above-noted project, please find the Final Monitoring Report for the community of Kettle and Stony Point First Nation and Lambton Shores.

Sincerely,

[original signed by]

Shelley Bechard Administrative Analyst, Regulatory Projects

cc: Z. Crnojacki N. Marconi Regulatory Library

KETTLE POINT/ LAMBTON SHORES NATURAL GAS PIPELINE PROJECT

FINAL MONITORING REPORT

Prepared By: Enbridge Gas Inc. Environmental Planning March 2019

TABLE OF CONTENTS

Kettle Point/ Lambton Shores Natural Gas Pipeline Project Final Monitoring Report

1.0 Introduction
2.0 Background
3.0 Potential Impacts and Mitigation
3.1 Condition 1
3.2 Condition 3
3.3 Condition 4
3.4 Condition 6
4.0 Summary

Table 1 – Potential Impacts and Mitigation MeasuresAppendix A – General Location MapAppendix B – Conditions of ApprovalAppendix C – Change Requests and Approvals

Appendix D – Executive Certification

1.0 INTRODUCTION

This Final Monitoring Report is provided in compliance with the Ontario Energy Board ("OEB") Order EB-2015-0179 granting Union Gas Limited ("Union") "Leave to Construct" 20.3 kilometres of new natural gas pipeline consisting of 10.4 kilometres of Nominal Pipe Size (NPS) 4 inch plastic pipeline and 9.9 kilometres of NPS 2 inch plastic pipeline to provide natural gas service to Kettle and Stony Point First Nation and the Ipperwash Beach area of Lambton Shores.

The NPS 4 inch plastic pipeline commenced at Union's existing pipeline/new distribution station at the southwest corner of Army Camp Road and Ravenswood Line. The pipeline travelled west along Ravenswood Line, with one section continuing north along Ipperwash Road to service Ipperwash Beach and another section travelling west along Lakeshore Road to service Kettle and Stony Point First Nation. NPS 2 inch plastic pipeline was installed in both communities. All pipelines were installed within road allowances with the exception of the three easements obtained as described in Change Request #5 in Appendix C. Union also obtained fee simple rights to construct the distribution station on private land. Please see Appendix A for a map of the entire pipeline route.

The requirements for and details of this report are outlined in the specific conditions issued by the OEB in its Order dated August 10, 2017 and as listed below. The complete Conditions of Approval can be found in Appendix B. The Conditions of Approval addressed in this report are as follows:

Condition 1

Union Gas Limited (Union) shall construct the facilities and restore the land in accordance with the OEB's Decision and Order in EB-2015-0179 and these Conditions of Approval.

Condition 3

Union shall implement all the recommendations of the Environmental Protection Plan filed in the proceeding.

Condition 4

Union shall advise the OEB of any proposed change to OEB-approved construction or restoration procedures. Except in an emergency, Union shall not make any such change without prior notice to and written approval of the OEB. In the event of an emergency, the OEB shall be informed immediately after the fact.

Condition 6

Both during and after construction, Union shall monitor the impacts of construction, and shall file with the OEB one paper copy and one electronic (searchable PDF) version of each of the following reports:

- a) a post construction report, within three months of the in-service date, which shall:
 - i. provide a certification, by a senior executive of the company, of Union adherence to Condition 1;
 - ii. describe any impacts and outstanding concerns identified during construction;
- iii. describe the actions taken or planned to be taken to prevent or mitigate any identified impacts of construction;
- iv. include a log of all complaints received by Union, including the date/time the complaint was received, a description of the complaint, any actions taken to address the complaint, the rationale for taking such actions; and
- v. provide a certification, by a senior executive of the company, that the company has obtained all other approvals, permits, licenses, and certificates required to construct, operate and maintain the proposed project.
- b) a final monitoring report, no later than 15 months after the in-service date, or, where the deadline falls between December 1 and May 31, the following June 1, which shall:
 - i. provide a certification, by a senior executive of the company, of Union adherence to Condition 3;
 - ii. describe the condition of any rehabilitated land;
- iii. describe the effectiveness of any actions taken to prevent or mitigate any identified impacts of construction;

- iv. include the results of analyses and monitoring programs and any recommendations arising therefrom; and
- v. include a log of all complaints received by Union, including the date/time the complaint was received, a description of the complaint, any actions taken to address the complaint, the rationale for taking such actions.

2.0 BACKGROUND

Union was granted approval to construct the Kettle Point/Lambton Shores Natural Gas Pipeline Project on August 10, 2017. Construction was initiated on September 18, 2017 and the pipeline was placed into service on December 19, 2017. Cleanup and land restoration was completed concurrently to construction, and was completed for the year on December 19, 2017. Cleanup along the pipeline route continued in spring 2018 and was completed by fall 2018.

Construction commenced at Army Camp Road and Ravenswood Line with the installation of NPS 4 inch plastic pipeline and continued west along Lakeshore Road to Kettle Point. Construction then continued simultaneously with the installation of NPS 2 inch pipeline in Kettle Point and the installation of NPS 4 inch pipeline along Ipperwash Road and then the installation of NPS 2 inch pipeline in Ipperwash Beach. Construction generally progressed with the following order of operations: flagging/staking, stringing, trenching/HDD, lowering-in, tie-ins, back filling, and clean-up.

Union ensured that all clean-up and restoration measures were successful and all disturbed areas were stable and re-vegetated. Any areas requiring additional restoration measures were addressed in spring/summer 2018 and there are no outstanding concerns.

3.0 POTENTIAL IMPACTS AND MITIGATION

3.1 <u>Condition 1</u>

Union Gas Limited (Union) shall construct the facilities and restore the land in accordance with the OEB's Decision and Order in EB-2015-0179 and these Conditions of Approval.

Union has constructed the facilities and restored the land in accordance with the OEB's Decision and Order in EB-2015-0179 and these Conditions of Approval, including the conditions from the change requests approvals as discussed in section 3.3.

3.2 Condition 3

Union shall implement all the recommendations of the Environmental Protection Plan filed in the proceeding.

Union has implemented all the recommendations of the Environmental Protection Plan filed in the proceeding. Please refer to Table 1 to confirm Union's adherence to the recommendations and mitigation measures identified in the Environmental Protection Plan.

3.3 <u>Condition 4</u>

Union shall advise the OEB of any proposed change to OEB-approved construction or restoration procedures. Except in an emergency, Union shall not make any such change without prior notice to and written approval of the OEB. In the event of an emergency, the OEB shall be informed immediately after the fact.

Union advised the Board of three (3) changes to the Board – approved construction procedures on September 19, 2017 (2) and November 27, 2017 (1). Union received Board approval for the first two change requests on September 29, 2017 and the third change request on November 30, 2017. Union's change requests and Board approvals are presented in Appendix C.

3.4 <u>Condition 6</u>

Both during and after construction, Union shall monitor the impacts of construction and shall file with the OEB one paper copy and one electronic (searchable PDF) version of each of the following reports:

- a) a post construction report, within three months of the in-service date, which shall:
 - *i.* provide a certification, by a senior executive of the company, of Union adherence to Condition 1;

- *ii. describe any impacts and outstanding concerns identified during construction;*
- *iii. describe the actions taken or planned to be taken to prevent or mitigate any identified impacts of construction;*
- *iv.* Include a log of all complaints received by Union, including the date/time the complaint was received, a description of the complaint, any actions taken to address the complaint, the rationale for taking such actions; and
- v. provide a certification, by a senior executive of the company, that the company has obtained all other approvals, permits, licenses, and certificates required to construct, operate and maintain the proposed project.

A Post Construction Report was filed with the OEB within three months of the December 19, 2017 in-service date.

- b) a final monitoring report, no later than 15 months after the in-service date, or, where the deadline falls between December 1 and May 31, the following June 1, which shall:
 - *i.* provide a certification, by a senior executive of the company, of Union adherence to Condition 3;

One paper copy and one electronic (searchable PDF) version of this Final Monitoring Report are provided to the Board. This report is certified by Jim Sanders, Senior Vice President of Operations, that Union has implemented all the recommendations of the Environmental Protection Plan filed in the proceeding and is confirmed by the signed letter of approval found in Appendix D.

ii. describe the condition of any rehabilitated land;

All disturbed areas were restored as soon as possible upon completion of pipe installation. Vegetative cover was restored by means of seeding and sodding where required. Native seed mixes suitable to a roadside environment were used along roadways and sod was used where required in residential areas. All disturbed areas were successfully rehabilitated and no further cleanup is required.

iii. describe the effectiveness of any actions taken to prevent or mitigate any identified impacts of construction;

The mitigation measures taken to address the identified impacts of construction as listed in Table 1 were utilized and successful. No actions outside of the mitigation measures listed in Table 1 were necessary to prevent or mitigate any identified impacts of construction.

iv. include the results of analyses and monitoring programs and any recommendations arising therefrom; and

Union's standard well monitoring program was in effect during construction. No complaints related to water well quantity or quality were reported during construction. No other post construction monitoring programs were required.

v. include a log of all complaints received by Union, including the date/time the complaint was received, a description of the complaint, any actions taken to address the complaint, the rationale for taking such actions.

Union's Complaint Tracking System, which identifies the current status of complaints received as a result of pipeline construction, was in effect. A complaint is identified as a concern raised by a landowner or member of the public that has not been resolved to their satisfaction within three (3) working days. No complaints were received during construction and therefore a log of complaints was not produced.

During construction and clean-up, a number of concerns were raised to Union and their Contractor. These issues were minor in nature and were dealt with by Union and the Contractor in an expeditious manner and there are no outstanding concerns. Kettle Point/ Lambton Shores Natural Gas Pipeline Project Final Monitoring Report

4.0 <u>SUMMARY</u>

This Final Monitoring Report has been prepared as per conditions in the Board Order EB-2015-0179. The report provides confirmation that Union has implemented all the recommendations of the Environmental Protection Plan filed in the proceeding, including the mitigation measures which prevented or mitigated the identified impacts of construction. This report also confirms that Union successfully rehabilitated the land disturbed from construction and there are no outstanding concerns. It is anticipated that these mitigation measures and rehabilitation efforts will effectively eliminate any long-terms impacts to the environment.

Table 1

Potential Impacts and Mitigation Measures

Table 1: Potential Impacts and Mitigation Measures Issue Potential Impact Mitigation Measure			
	Potential Impact	Mitigation Measure	
Paved/Gravel Driveways and	Disruption to local traffic, landowners and tenants	- All roadways and driveways were bored if practical.	
Roadways		- If it was not possible to bore driveways and roads, steel plates were on site to provide access to landowners and tenants.	
		 The Company kept at least one lane of traffic open during construction and traffic controls were implemented as required. 	
		- For driveways that required cutting, the excavation was filled with sand and	
		 granular material and compacted. Driveways were repaired as soon as possible. 	
Traffic	Disruption to local citizens	- At least one lane of traffic was maintained at all times.	
		- Flag persons and warning devices were used to notify traffic of construction in accordance with Ministry of Transportation standards.	
Public Safety	Public safety concerns	 Company inspectors ensured public safety on the construction site. Proper signage and flag persons were 	
		used where required.	
Commercial/Retail Businesses and Recreational Areas	Disruption to businesses	 Access to businesses was maintained at all times. The land around businesses and recreational areas was restored as soon 	
		as possible.	
Construction Noise	Disturbance to local citizens	- Construction was carried out during daylight hours whenever possible.	
		- Equipment was properly muffled.	
Nuisance Dust	Disturbance to local citizens	- Dust was controlled as required.	
Construction Equipment	Disturbance to local citizens	- Equipment was stored off road shoulders when not in use.	
Landowner Concerns	Disruption to landowners (First Nation/ Municipality)	- The Company provided the First Nation/ Municipality with the telephone numbers of supervisory personnel.	
Fences	Disruption to landowners	 No fences were removed or damaged during construction. 	
	Loss of control of animals inside fenced areas	-	


Table 1: Potential Impacts and Mitigation Measures				
Issue	Potential Impact	Mitigation Measure		
Front Yards	Disruption to landowners and tenants	 Landowners and tenants were notified prior to construction. Lawns and yards were restored to original condition. 		
Mailboxes	Disruption to landowners and tenants	 Landowners were notified of mailbox disruption when required. Mailboxes were restored as soon as possible and temporary alternatives were provided if necessary. 		
Underground Utilities	Disruption of services	 Locates were obtained from all utilities. Any damages to utilities were repaired as soon as possible. 		
Archaeology	Disturbance of heritage resources	 An Archaeological Assessment was completed prior to construction. No artifacts were encountered during construction. 		
Water Wells	Disruption to water supply	 A hydrogeological investigation was conducted prior to construction. No water well problems were reported during construction. 		
Trees	Damage to trees Disturbance to wildlife	- Tree removal did not occur as part of construction.		
Watercourse Crossings	Water quality concerns	 Union complied with all permit conditions from the Ausable Bayfield Conservation Authority and St. Clair Region Conservation Authority. Union adhered to all Company specifications and the Fisheries and Oceans Canada – endorsed Generic Sediment Control Plan for Horizontal Directional Drill for watercourse crossings. 		
Natural Areas	Sedimentation run-off	- Sediment barriers (i.e. silt fencing and filter socks) were used in areas where there was potential for run-off.		
Vegetative Cover	Loss of vegetative cover leading to soil erosion	- Cover was restored by seeding as soon as possible.		
Soils: Erosion	Introduction of sediment/silt to adjacent lands	- Disturbed soils were restored as soon as possible after construction.		
Roadside Ditches	Water quality concerns	- Ditches were returned to pre- construction condition as quickly as possible.		

Table 1: Potential Impacts and Mitigation Measures				
Issue	Potential Impact	Mitigation Measure		
		- Rock rip rap/straw bale check dams were installed as required.		
Spills	Public safety issue	- No spills were identified during construction.		
Contaminated Soils	Dealing with contaminated materials Public safety issue	 No contaminated soils were identified during construction. 		
Cemeteries	Disturbance to unmarked grave sites and disruption to services	 Archaeological Assessments were conducted around cemeteries to prevent potential impacts. Construction was suspended during services. 		
Site Restoration	Disturbance to public and private properties	- The construction area was restored as soon as possible upon completion of pipe installation.		

Appendix A

General Location Map

Kettle Point & Lambton Shores - Community Expansion Key Plan

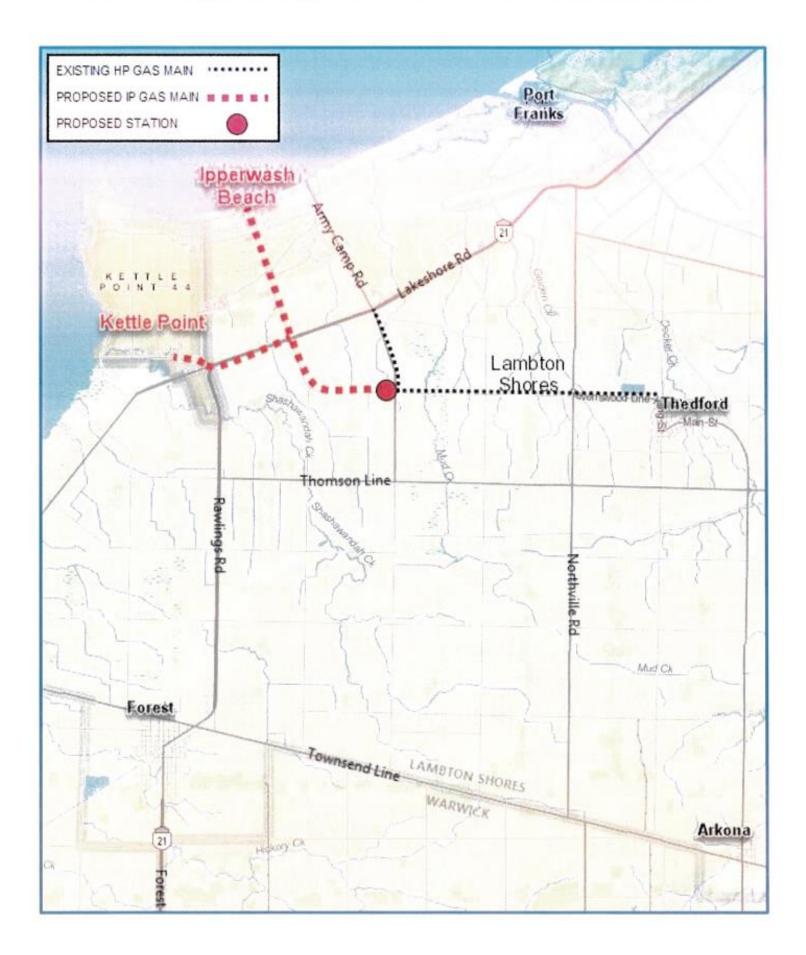

Appendix B

Conditions of Approval

Leave to Construct Conditions of Approval Application under Section 90 of the *Ontario Energy Board Act, 1998* Union Gas Limited EB-2015-0179

- Union Gas Limited (Union) shall construct the facilities and restore the land in accordance with the OEB's Decision and Order in EB-2015-0179 and these Conditions of Approval.
- a) Authorization for leave to construct shall terminate 12 months after the decision is issued, unless construction has commenced prior to that date.
 - b) Union shall give the OEB notice in writing:
 - of the commencement of construction, at least 10 days prior to the date construction commences;
 - ii. of the planned in-service date, at least 10 days prior to the date the facilities go into service;
 - iii. of the date on which construction was completed, no later than 10 days following the completion of construction; and
 - iv. of the in-service date, no later than 10 days after the facilities go into service.
- Union shall implement all the recommendations of the Environmental Protection Plan filed in the proceeding.
- 4. Union shall advise the OEB of any proposed change to OEB-approved construction or restoration procedures. Except in an emergency, Union shall not make any such change without prior notice to and written approval of the OEB. In the event of an emergency, the OEB shall be informed immediately after the fact.
- 5. Union shall file, in the proceeding where actual capital costs of the project are proposed to be included in rate base, a Post Construction Financial Report, which shall indicate the actual capital costs of the project and shall provide an explanation of any significant variances from the cost estimates filed in this proceeding.
- Both during and after construction, Union shall monitor the impacts of construction, and shall file with the OEB one paper copy and one electronic (searchable PDF) version of each of the following reports:
 - a) a post construction report, within three months of the in-service date, which shall:

- provide a certification, by a senior executive of the company, of Union adherence to Condition 1;
- ii. describe any impacts and outstanding concerns identified during construction;
- iii. describe the actions taken or planned to be taken to prevent or mitigate any identified impacts of construction;
- iv. include a log of all complaints received by Union, including the date/time the complaint was received, a description of the complaint, any actions taken to address the complaint, the rationale for taking such actions; and
- provide a certification, by a senior executive of the company, that the company has obtained all other approvals, permits, licenses, and certificates required to construct, operate and maintain the proposed project.
- b) a final monitoring report, no later than 15 months after the in-service date, or, where the deadline falls between December 1 and May 31, the following June 1, which shall:
 - provide a certification, by a senior executive of the company, of Union adherence to Condition 3;
 - ii. describe the condition of any rehabilitated land;
 - iii. describe the effectiveness of any actions taken to prevent or mitigate any identified impacts of construction;
 - iv. include the results of analyses and monitoring programs and any recommendations arising therefrom; and
 - v. include a log of all complaints received by Union, including the date/time the complaint was received, a description of the complaint, any actions taken to address the complaint, the rationale for taking such actions.

Appendix C

Change Requests and Approvals



September 19, 2017

RESS & COURIER

Ms. Kirsten Walli Board Secretary Ontario Energy Board 2300 Yonge Street, 27th Floor Toronto, ON M4P 1E4

Dear Ms. Walli,

Re: Union Gas Limited ("Union") Community Expansion Project Board File # EB-2015-0179

Please find attached three change requests, for the above-noted project.

Union believes that these changes are not significant and would appreciate your timely review and approval of this request, as construction is in progress. Confidential copies of the redacted schedules are being couriered to the Board seperately.

In the event that you have any questions or would like to discuss in more detail, please do not hesitate to contact me.

Sincerely,

[original signed by]

W.T. (Bill) Wachsmuth, RPF Senior Administrator, Regulatory Projects

cc: Zora Crnojacki, OEB Nancy Marconi, OEB Ritchie Murray, OEB

REQUEST TO VARY

 Project Name:
 Kettle and Stony Point First Nation and Lambton Shores
Community Expansion Project

 OEB file Number:
 EB-2015-0179

Request to Vary: 1

Description and Rationale for Change

Union requires a different area of land for construction of the proposed station at the north end of the proposed facilities. In Union's original application it assumed a square piece of property would be available at the corner of Army Camp Road and Ravenswood Line. Union was not aware that the municipality had obtained land at this corner and that the corner was now "daylighted". Union is proposing to construct the station within the private property adjacent to the" daylighted" road allowance.

Construction and Restoration Practices

Union's standard construction practices will be followed for construction of the station facilities.

Environmental

No new environmental mitigation measures will be required.

Consultation

Union has discussed this change with the affected landowner and the municipality. No concerns have been identified.

Lands

The landowner has sold Union the property required for the station.

Costs

Union had always proposed the station at this location changing the shape and size of the property Union purchased did not result in any additional costs.

Schedule

This change will not result in a change to the in-service date of the project.

Attachments

A survey drawing showing the new location of the station is attached at Schedule 1.

REQUEST TO VARY

 Project Name:
 Kettle and Stony Point First Nation and Lambton Shores Community Expansion Project

 OEB file Number:
 EB-2015-0179

Request to Vary: 3

Description and Rationale for Change

Union has been working with the Municipality of Lambton Shores and the Kettle and Stony Point First Nation to refine the pipeline plan for the project area. These discussions have resulted in a number of changes to the plan which was filed in March 2017. A map showing the revised pipeline plan can be found at Schedule 1.

In some instances Union is proposing to pipe both sides of some streets to shorten service connections. Whereas in other instances Union is proposing to pipe only one side of the street. Other changes have also been implemented in order to make construction more efficient.

In reviewing the revised plan Union can confirm that every resident and business who had access to natural gas service in the original plan, still has access to natural gas service.

Construction and Restoration Practices

Union's standard construction practices will be followed for construction of the pipeline facilities.

Environmental

No new environmental mitigation measures will be required.

Consultation

Union has discussed this change with the municipality and the First Nation. No concerns have been identified.

Lands

No additional permanent or temporary easements are required to implement this change.

Costs

These changes will not result in any costs increases to the project.

Schedule

This change will not result in a change to the in-service date of the project.

Attachments

A drawing showing the new location for the pipelines is attached at Schedule 1.

Ontario Energy Board P.O. Box 2319 27th Floor 2300 Yonge Street Toronto ON M4P 1E4 Telephone: 416-481-1967 Facsimile: 416-440-7656 Toll free: 1-888-632-6273 Commission de l'énergie de l'Ontario C.P. 2319 27^e étage 2300, rue Yonge Toronto ON M4P 1E4 Téléphone: 416-481-1967 Télécopieur: 416-440-7656 Numéro sans frais: 1-888-632-6273



BY E-MAIL

September 29, 2017

Bill Wachsmuth Union Gas Limited Senior Administrator, Regulatory Projects 50 Keil Drive North P.O. Box 2001 Chatham ON N7M 5M1 <u>bwachsmuth@uniongas.com</u>

Dear Mr. Wachsmuth:

Re: Community Expansion Project – EB-2015-0179 Request to Vary Change Request Nos. 1, 2 and 3

The Ontario Energy Board (OEB) is in receipt of your letter dated September 19, 2017 in which Union Gas Limited (Union) advised the OEB of three changes to the Community Expansion Project (Change Request Nos. 1, 2 and 3).

As the Manager, Applications Policy and Climate Change, I have been delegated the authority of the OEB under section 6 of the Ontario Energy Board Act, 1998 to determine whether Union's proposals will result in material changes to the leave to construct granted by the OEB in the EB-2016-0179 proceeding. I have been further granted the authority to approve any changes that I have concluded are not material.

I address each of the three change requests in the following sections.

Change Request No. 1

This request pertains to the Kettle and Stony Point First Nation and Lambton Shores Community Expansion Project. It involves the relocation of a pressure regulating station. The location originally intended for the station is located in the apex of the south west corner of the intersection of Army Camp Road and Ravenswood Line. Subsequent to its LTC application, Union has learned that the apex is required by the municipality to provide "daylighting", or the ability for motorists to have an unobstructed view throughout the intersection. As a result, Union proposes to reorient and relocate the station within the private property adjacent to the "daylighted" road allowance.

Union has indicated the following:

- 1. This change will not modify the project's construction methods, environmental mitigation measures, costs or schedule
- Union has discussed the change with affected landowners and the municipality; no concerns were identified
- 3. Union has purchased the necessary land

Based on my review of the information provided, I find that the described change does not materially impact the leave granted by the OEB to construct the pipeline. I hereby approve the proposed change.

Change Request No. 2

This request pertains to the Milverton Rostock Wartburg Community Expansion Project. In an effort to minimize disturbance to business, Union proposes to serve certain areas of downtown Milverton by using side streets and laneways rather than using main streets as originally proposed. Additionally, Union is proposing to serve two new subdivisions off the Milverton distribution system sooner than originally planned.

Union has indicated the following:

- These changes will not modify the project's construction methods, environmental mitigation measures, or schedule
- These changes will increase the first year project costs by \$40,000; however, the 10year project costs are not materially changed as some of these pipelines were planned to be constructed in later years
- Union has discussed the changes with affected landowners and the municipality; no concerns were identified
- 4. With one exception, Union has acquired additional land rights and filed copies of the executed landowner agreements. The form of easement agreement for the additional Land Rights was approved by the OEB in its February 23, 2017 Decision and Order in Union's Panhandle Replacement Project (EB-2016-0186). The one exception is a landowner who is currently out of the country but has committed in an email to signing an easement agreement by the end of September, 2017
- Every resident and business who would have had access to gas under the original plan will have access to gas if the changes are approved

Based on my review of the information provided, I find that the described changes do not materially impact the leave granted by the OEB to construct the pipeline. I hereby approve the proposed changes.

Change Request No. 3

This request pertains to the Kettle and Stony Point First Nation and Lambton Shores Expansion Project. It involves changes intended to make construction more efficient (for example installing pipe on both sides of certain streets to shorten service connections).

Union has indicated the following:

- These changes will not modify the project's construction methods, environmental mitigation measures, project costs or schedule
- The proposed changes do not alter the project's permanent or temporary land use requirements as construction remains within the previously disturbed portions of the road allowance
- Union has discussed the changes with the municipality and the First Nation; no concerns were identified
- Every resident and business who would have had access to gas under the original plan will have access to gas if the changes are approved

Based on my review of the information provided, I find that the described changes do not materially impact the leave granted by the OEB to construct the pipeline. I hereby approve the proposed changes.

Yours truly,

Original Signed by

Pascale Duguay Manager, Applications Policy and Climate Change



November 27, 2017

RESS & COURIER

Ms. Kirsten Walli Board Secretary Ontario Energy Board 2300 Yonge Street, 27th Floor Toronto, ON M4P 1E4

Dear Ms. Walli,

Re: Union Gas Limited ("Union") Community Expansion Project Board File # EB-2015-0179

Please find attached Change Request #5, for the above-noted project.

Union believes that this change is not significant and would appreciate your timely review and approval of this request, as construction is in progress. Confidential copies of Schedule 2 are being couriered to the Board separately.

In the event that you have any questions or would like to discuss in more detail, please do not hesitate to contact me.

Sincerely,

[original signed by]

W.T. (Bill) Wachsmuth, RPF Senior Administrator, Regulatory Projects

ce: Zora Crnojacki, OEB Nancy Marconi, OEB Ritchie Murray, OEB

REQUEST TO VARY

Project Name:	Kettle and Stony Point First Nation and Lambton Shores Community Expansion Project
OEB file Number:	EB-2015-0179
Request to Vary:	5

Description and Rationale for Change

Union has had requests to provide natural gas service to four additional roads within the boundaries of the Kettle and Stony Point First Nation and Lambton Shores Project Area. These requests can be completed without changing the Project economics filed as part of Union's pre-filed evidence.

Three of the areas; Wolfe Drive, Culbert Street, and West Ipperwash Beach Road will be constructed on or adjacent to existing roadways. The fourth area will be constructed along a private laneway for which Union was able to obtain signed easements from the affected landowners. A map showing the location of these areas can be found at Schedule 1.

Construction and Restoration Practices

Union's standard construction practices will be followed for construction of the proposed pipelines.

Environmental

No new environmental mitigation measures will be required.

Consultation

Union has discussed this change with the affected landowners, Municipality and Kettle and Stony Point First Nation. They did not identify any concerns.

Lands

Union requires three easements to construct the pipeline along the private laneway. Copies of these signed easements can be found at Schedule 2.

Costs

Construction of these additional pipelines will increase the Project costs by approximately \$100,000. A DCF analysis has been completed using these additional costs and the revenues associated with the additional customers that will be attached in these four areas and the PI of the Project remains positive.

Schedule

This change will not result in a change to the in-service date of the project.

Attachments

A drawing showing the location of the proposed pipeline is attached at Schedule 1. Copies of the signed easements are attached at Schedule 2. Ontario Energy Board P.O. Box 2319 27th Floor 2300 Yonge Street Toronto ON M4P 1E4 Telephone: 416-481-1967 Facsimile: 416-440-7656 Toll free: 1-888-632-6273 Commission de l'énergie de l'Ontario C.P. 2319 27^e étage 2300, rue Yonge Toronto ON M4P 1E4 Téléphone: 416-481-1967 Télécopieur: 416-440-7656 Numéro sans frais: 1-888-632-6273



BY E-MAIL

November 30, 2017

Bill Wachsmuth Senior Administrator, Regulatory Projects Union Gas Limited 50 Keil Drive North P.O. Box 2001 Chatham ON N7M 5M1 <u>bwachsmuth@uniongas.com</u>

Dear Mr. Wachsmuth:

Re: Community Expansion Project, EB-2015-0179 Request to Vary Change Request No. 5

The Ontario Energy Board (OEB) is in receipt of your letter dated November 27, 2017 in which Union Gas Limited (Union Gas) advised the OEB of a change to the Community Expansion Project (Change Request No. 5).

Union proposes to provide service to four additional roads within the boundaries of the Kettle and Stony Point First Nation and Lambton Shores Project Area. Union submits that this change will not modify the project's originally proposed construction or restoration methods, environmental mitigation measures, or project schedule. Project costs will increase by approximately \$100,000, however the project profitability index will remain positive. Three of the additional pipeline installations will be constructed on or adjacent to existing roadways. The fourth installation will be constructed along a private laneway for which Union has signed easement agreements with the three affected landowners.

As the Manager, Applications Supply and Infrastructure, I have been delegated the authority of the OEB under section 6 of the *Ontario Energy Board Act, 1998* to determine whether any proposed changes to OEB-approved construction or restoration procedures are material, and to approve any changes that I have concluded are not material.

Based on my review of the information provided, I have determined that the change proposed by Union Gas is not material. I approve the proposed change.

Yours truly,

Original Signed by

Nancy Marconi Manager, Applications Supply and Infrastructure

Appendix D

Executive Certification



Kettle Point/Lambton Shores Natural Gas Pipeline Project

EB-2015-0179

Decision and Order

August 10, 2017

I hereby certify that Enbridge Gas Inc. has implemented all the recommendations of the Environmental Protection Plan filed in the proceeding, as per Condition 6 (b)(i) of the Decision and Order, EB-2015-0179.

March 12, 2019 Date

Senior Executive

Condition 6 (b) (i)

- 6. Both during and after construction, Union shall monitor the impacts of construction, and shall file with the OEB one paper copy and one electronic copy (searchable PDF) version of each of the following reports:
 - a) a final monitoring report, no later than 15 months after the in-service date, or, where the deadline falls between December 1 and May 31, the following June 1, which shall:
 - i. provide a certification, by a senior executive of the company, of Union adherence to Condition 3;

Condition 3

Union shall implement all the recommendations of the Environmental Protection Plan filed in the proceeding.
