

Smart Meter Time of Use EnWin Utilities Ltd

For the Period to: 31-Aug-13

RPP Eligible Consumers:

Description	Residential	GS < 50kW Class	Total
Total Number of RPP-eligible consumers	77,243	7,131	84,374
Number of smart meters installed in the period	26	4	30
Number of smart meters registered with the MDM/R in the period	0	0	0
Number of RPP consumers being charged TOU prices added in the period	0	0	0
Total cumulative number of smart meters installed in the service area at the end of the period	78,152	7,541	85,693
Total cumulative number of smart meters registered with the MDM/R at the end of the period	0	0	0
Total cumulative number of consumers being charged TOU prices at the end of the period	0	0	0

Progress Report on SME Milestones

Activity	Original Scheduled Completion Date	Status	Expected Completion Date	Actual Completion Date
1. AMCC Internal Testing		Complete	July 30, 2010	July 30, 2010

Activity	Original Scheduled Completion Date	Status	Expected Completion Date	Actual Completion Date
2. CIS Internal Testing	September 4, 2013	Behind Schedule	December 13, 2013	

Activity	Yes or No?	Expected Completion Date	Actual Completion Date
3. MDM/R Registration Application submitted	Yes	January 1, 2010	January 1, 2010

Activity	Yes or No?	Status, if Yes	Expected Completion Date	Actual Completion Date
4. Enrolment Wave requested and confirmed (Note: the SME will either confirm the requested start date or suggest an alternate)	Yes	Complete	March 25, 2013	January 23, 2013

Activity	Original Scheduled Completion Date	Status	Expected Completion Date	Actual Completion Date
5. Unit Testing	September 12, 2013	Behind Schedule	September 12, 2013	

Activity	Original Scheduled Completion Date	Status	Expected Completion Date	Actual Completion Date
6. Submitted a completed Self Certification for Enrolment Testing SME_FORM_0007 (Note: This must be submitted at least one week prior to the confirmed enrolment wave start date)	August 26, 2013	Behind Schedule	August 26, 2013	

Activity	Original Scheduled Completion Date	Status	Expected Completion Date	Actual Completion Date
7. System Integration Testing (SIT)	September 18, 2013	Behind Schedule	November 1, 2013	

Activity	Original Scheduled Completion Date	Status	Expected Completion Date	Actual Completion Date
8. Qualification Testing (QT)	October 17, 2013	Behind Schedule	November 29, 2013	


Activity	Original Scheduled Completion Date	Status	Expected Completion Date	Actual Completion Date
9. Self Certification - Cutover	November 28, 2013	Behind Schedule	March 17, 2014	

Activity	Original Scheduled Completion Date	Status	Expected Completion Date	Actual Completion Date
10. Transition to Production Operations	March 26, 2014	Behind Schedule	April 28, 2014	

Additional Comments and Information

EnWin expects to meet the requirement to apply TOU pricing under the Standard Supply Service Code to all of its customers by April 30, 2014 as approved in application EB-2012-0405


EnStar Project Plan Time Line - Revised Aug 30, 2013

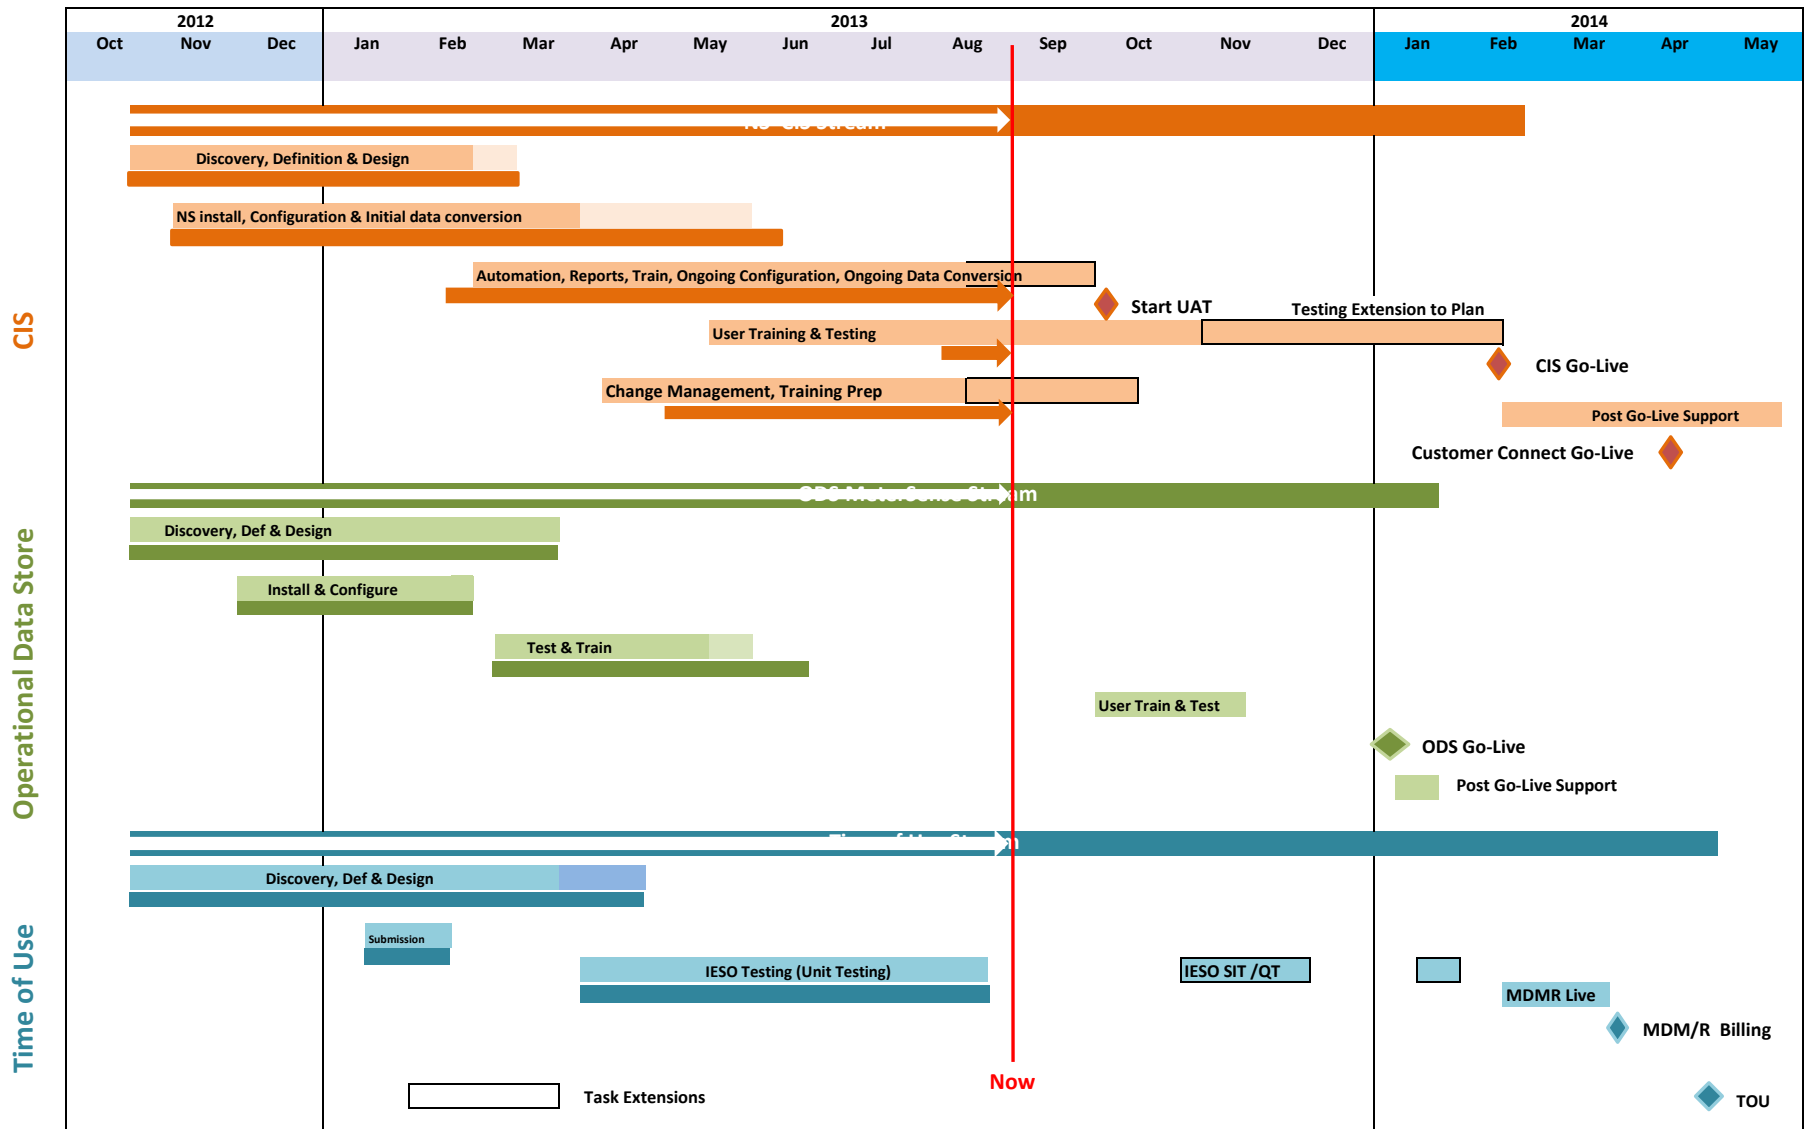


EnWin EnStar Project Plan - September 2013																
ID	% Complete	% Work Complete	Task Name	Start	Finish	Duration										
							03-24	07-14	11-03	02-23	October		06-15	10-05	01-25	05-17
1	64%	53%	Draft EnWin NorthStar Implementation Project Plan	Mon 12-10-15	Wed 14-06-25	85.1 wks?										
2																
3	100%	100%	START DATE (Tentative - Would need to be confirmed and reviewed at Contract Signature)	Mon 12-10-15	Mon 12-10-15	0 wks										
4	0%	0%	Milestone Validation section	Wed 13-09-04	Thu 14-02-20	23.2 wks										
5	0%	0%	CIS Accepted Solution (fixed)	Wed 13-09-04	Wed 13-09-04	0 wks										
6	0%	0%	CIS Accepted Solution tracked	Fri 13-12-20	Fri 13-12-20	0 wks										
7	0%	0%	CIS Go-Live (Fixed)	Mon 13-11-11	Mon 13-11-11	0 wks										
8	0%	0%	CIS Go-Live tracked	Tue 14-02-18	Tue 14-02-18	0 wks										
9	0%	0%	ERTH QT Complete (Fixed)	Mon 13-10-21	Mon 13-10-21	0 wks										
10	0%	0%	ERTH QT Complete tracked	Fri 13-11-29	Fri 13-11-29	0 wks										
11	0%	0%	MS Solution Live (fixed)	Thu 13-11-14	Thu 13-11-14	0 wks										
12	0%	0%	MS Solution Live tracked	Thu 14-02-20	Thu 14-02-20	0 wks										
13																
14	61%	46%	CIS Project	Mon 12-10-15	Wed 14-06-25	85.1 wks										
15	56%	56%	Project Management	Mon 12-10-15	Tue 14-03-11	70 wks										
16	56%	55%	Project Management / Technical Oversight / IT Environment Support	Mon 12-10-15	Tue 14-03-11	70 wks										
17	58%	55%	NS - Project Management	Mon 12-10-15	Tue 14-03-11	70 wks										
18	55%	55%	NS - Solution Oversight	Mon 12-10-15	Tue 14-02-04	65 wks										
19	55%	55%	NS - IT Environment Support	Mon 12-10-15	Tue 14-02-04	65 wks										
20	55%	55%	Communication Management	Mon 12-10-15	Tue 14-03-11	70 wks										
21	55%	55%	NS - Weekly Status Report	Mon 12-10-15	Tue 14-03-11	70 wks										
22	55%	55%	NS - Weekly Status Meeting	Mon 12-10-15	Tue 14-03-11	70 wks										
23	55%	55%	NS - Weekly Sponsor Meeting	Mon 12-10-15	Tue 14-03-11	70 wks										
24	55%	55%	NS - Monthly Steering Committee Meetings	Mon 12-10-15	Tue 14-03-11	70 wks										
25	56%	59%	Risk Management	Mon 12-10-15	Tue 14-02-04	65 wks										
26	100%	100%	NS - Create Risk Log	Mon 12-10-15	Fri 12-10-19	1 wk										
27	55%	55%	NS - Bi-Weekly Review of Risk Log	Mon 12-10-22	Tue 14-02-04	64 wks										
28	100%	100%	Project Plan	Mon 12-10-15	Fri 12-11-16	5 wks										
29	100%	100%	NS - Create/Update Master Project Plan (MDM/R, MS,	Mon 12-10-15	Fri 12-10-26	2 wks										
30	100%	100%	NS - Customer Review of Master Project Plan	Mon 12-10-29	Fri 12-11-02	1 wk										
31	100%	100%	NS - Update/Finalize Project Plan	Mon 12-11-05	Fri 12-11-16	2 wks										
32	100%	100%	NS - Milestone - Project Plan Reviewed / Updated	Fri 12-11-16	Fri 12-11-16	0 wks										
33	69%	42%	Deliverable/Acceptance Management	Mon 12-11-19	Tue 13-01-22	8 wks										


EnWin EnStar Project Plan - September 2013																				
ID	% Complete	% Work Complete	Task Name	Start	Finish	Duration									October					
							03-24	07-14	11-03	02-23	06-15	10-05	01-25	05-17	09-06	12-27				
37	0%	0%	NS - Acceptance Criteria Document Sign-Off	Wed 13-01-16	Tue 13-01-22	1 wk				0%										
38	0%	0%	NS - Deliverable - Acceptance Criteria Document	Tue 13-01-22	Tue 13-01-22	0 wks				01-22										
39	96%	99%	Solution Definition Phase	Mon 12-10-15	Mon 13-09-09	44.8 wks														
40	100%	100%	Project Preparation	Mon 12-10-15	Fri 12-10-19	0.85 wks				100%										
41	100%	100%	NS - Gather and Review Project Documentation	Mon 12-10-15	Thu 12-10-18	4 days				100%										
42	100%	100%	NS - Hold NorthStar internal Kick-Off Meeting	Fri 12-10-19	Fri 12-10-19	0.25 days				100%										
43	100%	100%	Project Kick-Off	Mon 12-10-15	Tue 12-10-23	1.4 wks				100%										
44	100%	100%	NS - Prepare and Schedule Project Kick-Off	Mon 12-10-15	Fri 12-10-19	5 days				100%										
45	100%	100%	NS - Hold Project Kick-Off	Mon 12-10-22	Tue 12-10-23	2 days				100%										
46	100%	100%	NS - Milestone - Kick-Off Meeting Held	Tue 12-10-23	Tue 12-10-23	0 wks				10-23										
47	100%	100%	NorthStar Product Orientation Session - Training	Mon 12-10-15	Thu 12-10-25	1.8 wks				100%										
48	100%	100%	NS - Schedule NS Product Orientation Session	Mon 12-10-15	Mon 12-10-15	0.25 days				100%										
49	100%	100%	NS - Prepare NS Product Orientation Training Session	Mon 12-10-15	Fri 12-10-19	1 wk				100%										
50	100%	100%	NS - Hold NS Product Orientation Session (session 1)	Wed 12-10-24	Thu 12-10-25	2 days				100%										
51	100%	100%	Discovery	Mon 12-10-15	Wed 12-11-07	3.6 wks				100%										
52	100%	100%	CIS Discovery	Mon 12-10-15	Wed 12-11-07	3.6 wks				100%										
59	94%	97%	CIS Definition	Thu 12-11-08	Mon 13-09-09	41.2 wks														
60	100%	100%	Physical Architecture Review / Recommendation	Mon 12-11-26	Tue 13-01-08	5 wks				100%										
64	100%	100%	Solution Requirements and Customizations Documents	Thu 12-11-08	Fri 13-01-04	7 wks				100%										
71	100%	100%	Reports Requirements Document	Thu 12-11-08	Fri 12-12-07	4.4 wks				100%										
77	100%	100%	Integration Requirements Document	Thu 12-11-08	Fri 13-01-04	7 wks				100%										
83	100%	100%	Conversion Requirements Document	Thu 12-11-08	Wed 12-12-12	5 wks				100%										
90	50%	59%	Training / Change Management Plan	Mon 13-01-07	Mon 13-09-09	34.2 wks														
96	100%	100%	Test Plan	Mon 13-01-07	Fri 13-02-01	4 wks				100%										
102	97%	98%	Customer Connect Definition	Mon 13-02-04	Mon 13-04-15	10 wks				97%										
103	100%	100%	NS - Customer Connect Overview Session	Mon 13-02-04	Wed 13-02-06	0.5 wks				100%										
104	100%	100%	NS - Requirements Review and Confirmation Session - Functional and Integration Requirements	Wed 13-02-06	Mon 13-02-11	0.7 wks				100%										
105	100%	100%	NS - Acceptance Criteria Items - Add to Main Project Document	Tue 13-02-12	Thu 13-02-14	0.5 wks				100%										
106	75%	75%	NS - Review and confirm Test Plan	Thu 13-02-14	Tue 13-02-19	0.5 wks				75%										
107	75%	75%	NS - Review and update Test Case Scenarios	Wed 13-02-20	Fri 13-02-22	0.5 wks				75%										
108	100%	100%	NS - Draft CustomerConnect Requirements Document	Tue 13-03-12	Mon 13-03-25	2 wks				100%										
109	100%	100%	NS - Review CustomerConnect Requirements Document	Tue 13-03-26	Mon 13-04-01	1 wk				100%										
Page 2																				

EnWin EnStar Project Plan - September 2013

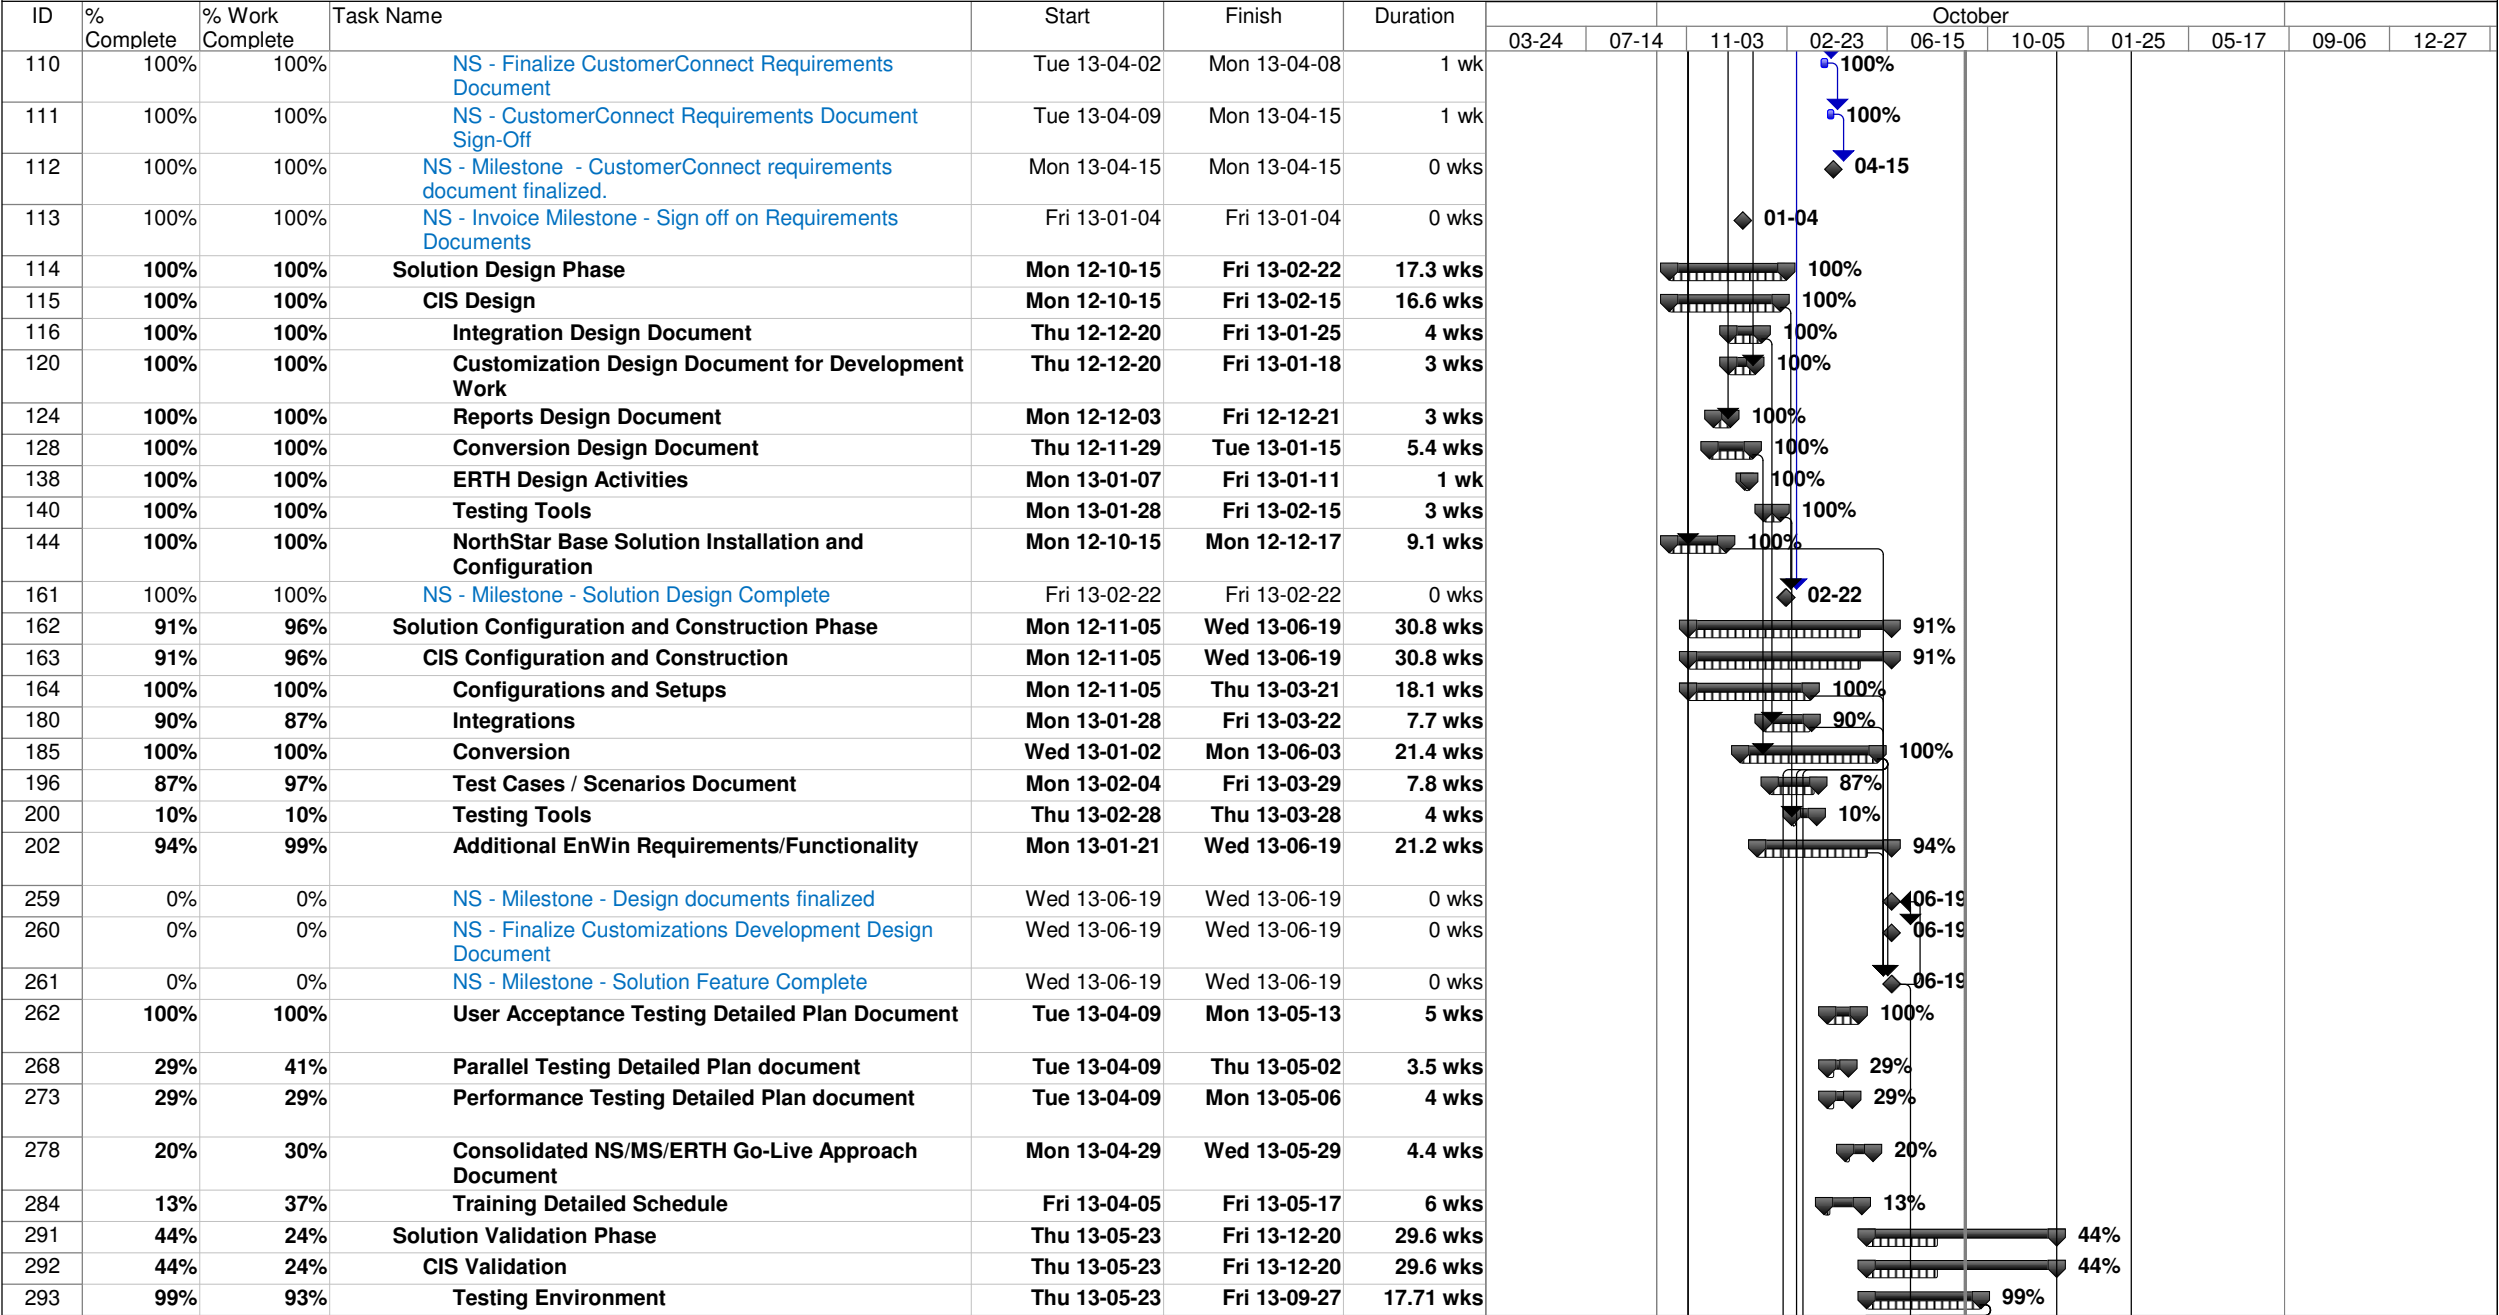

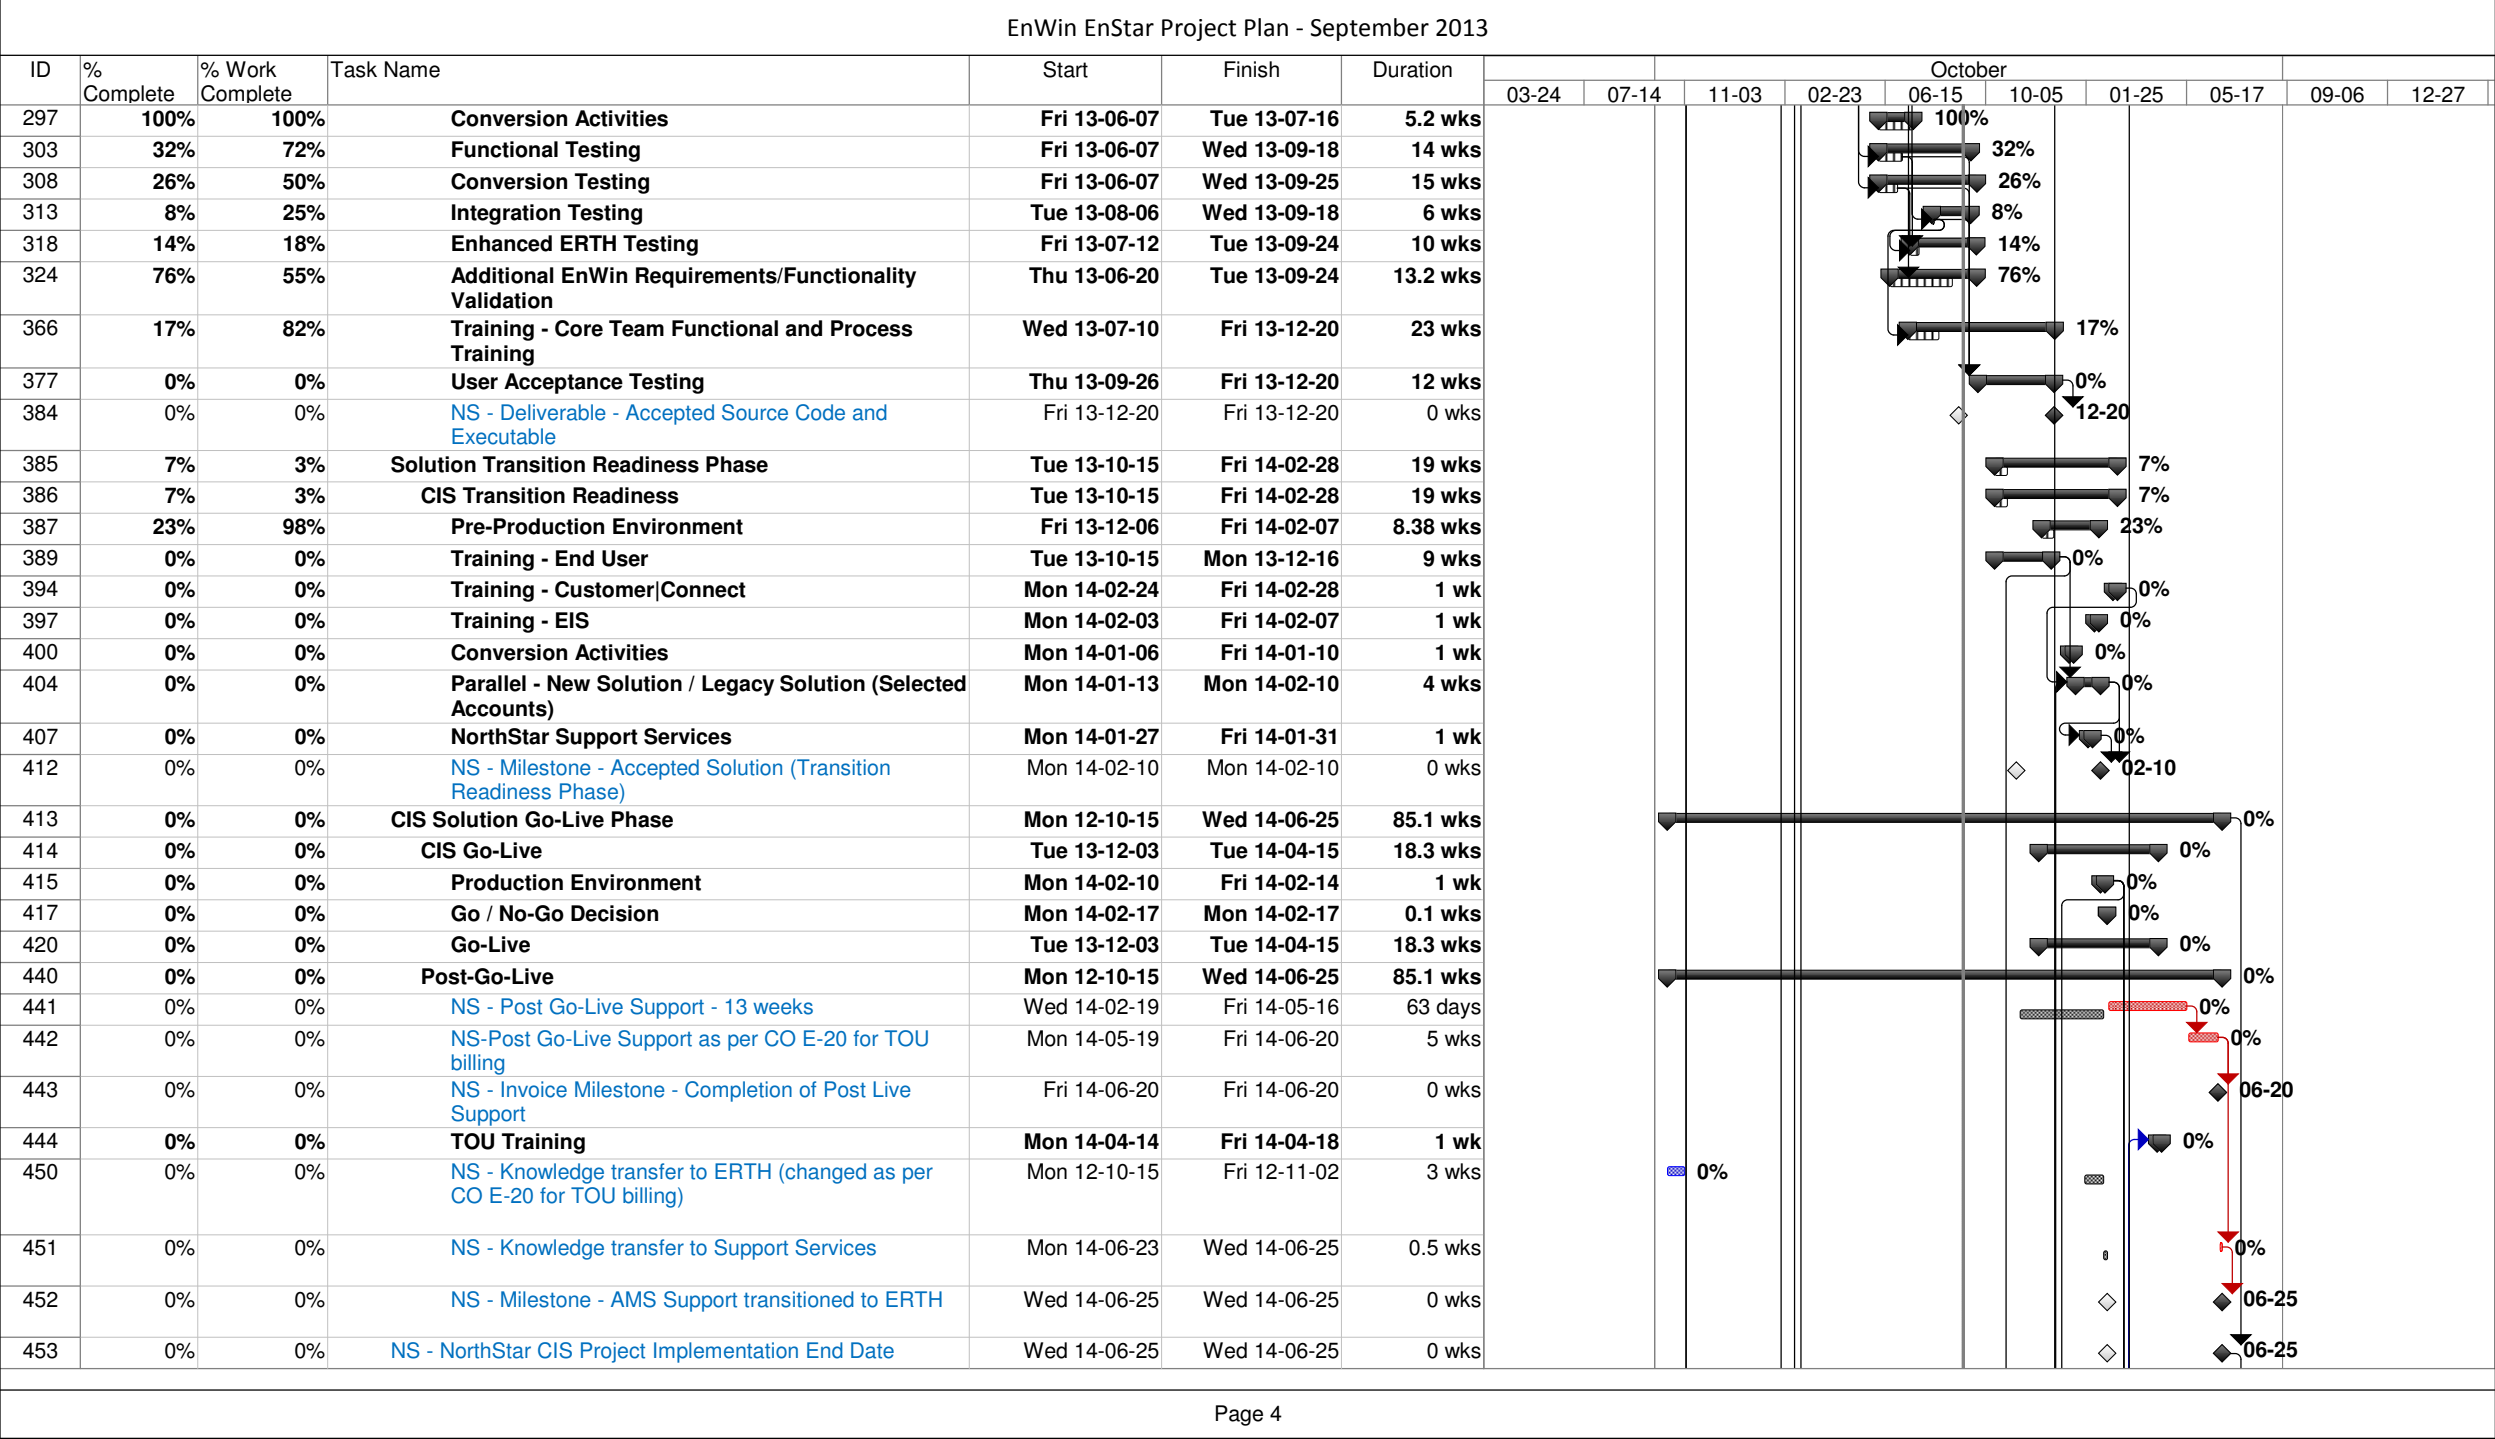


EnWin EnStar Project Plan - September 2013

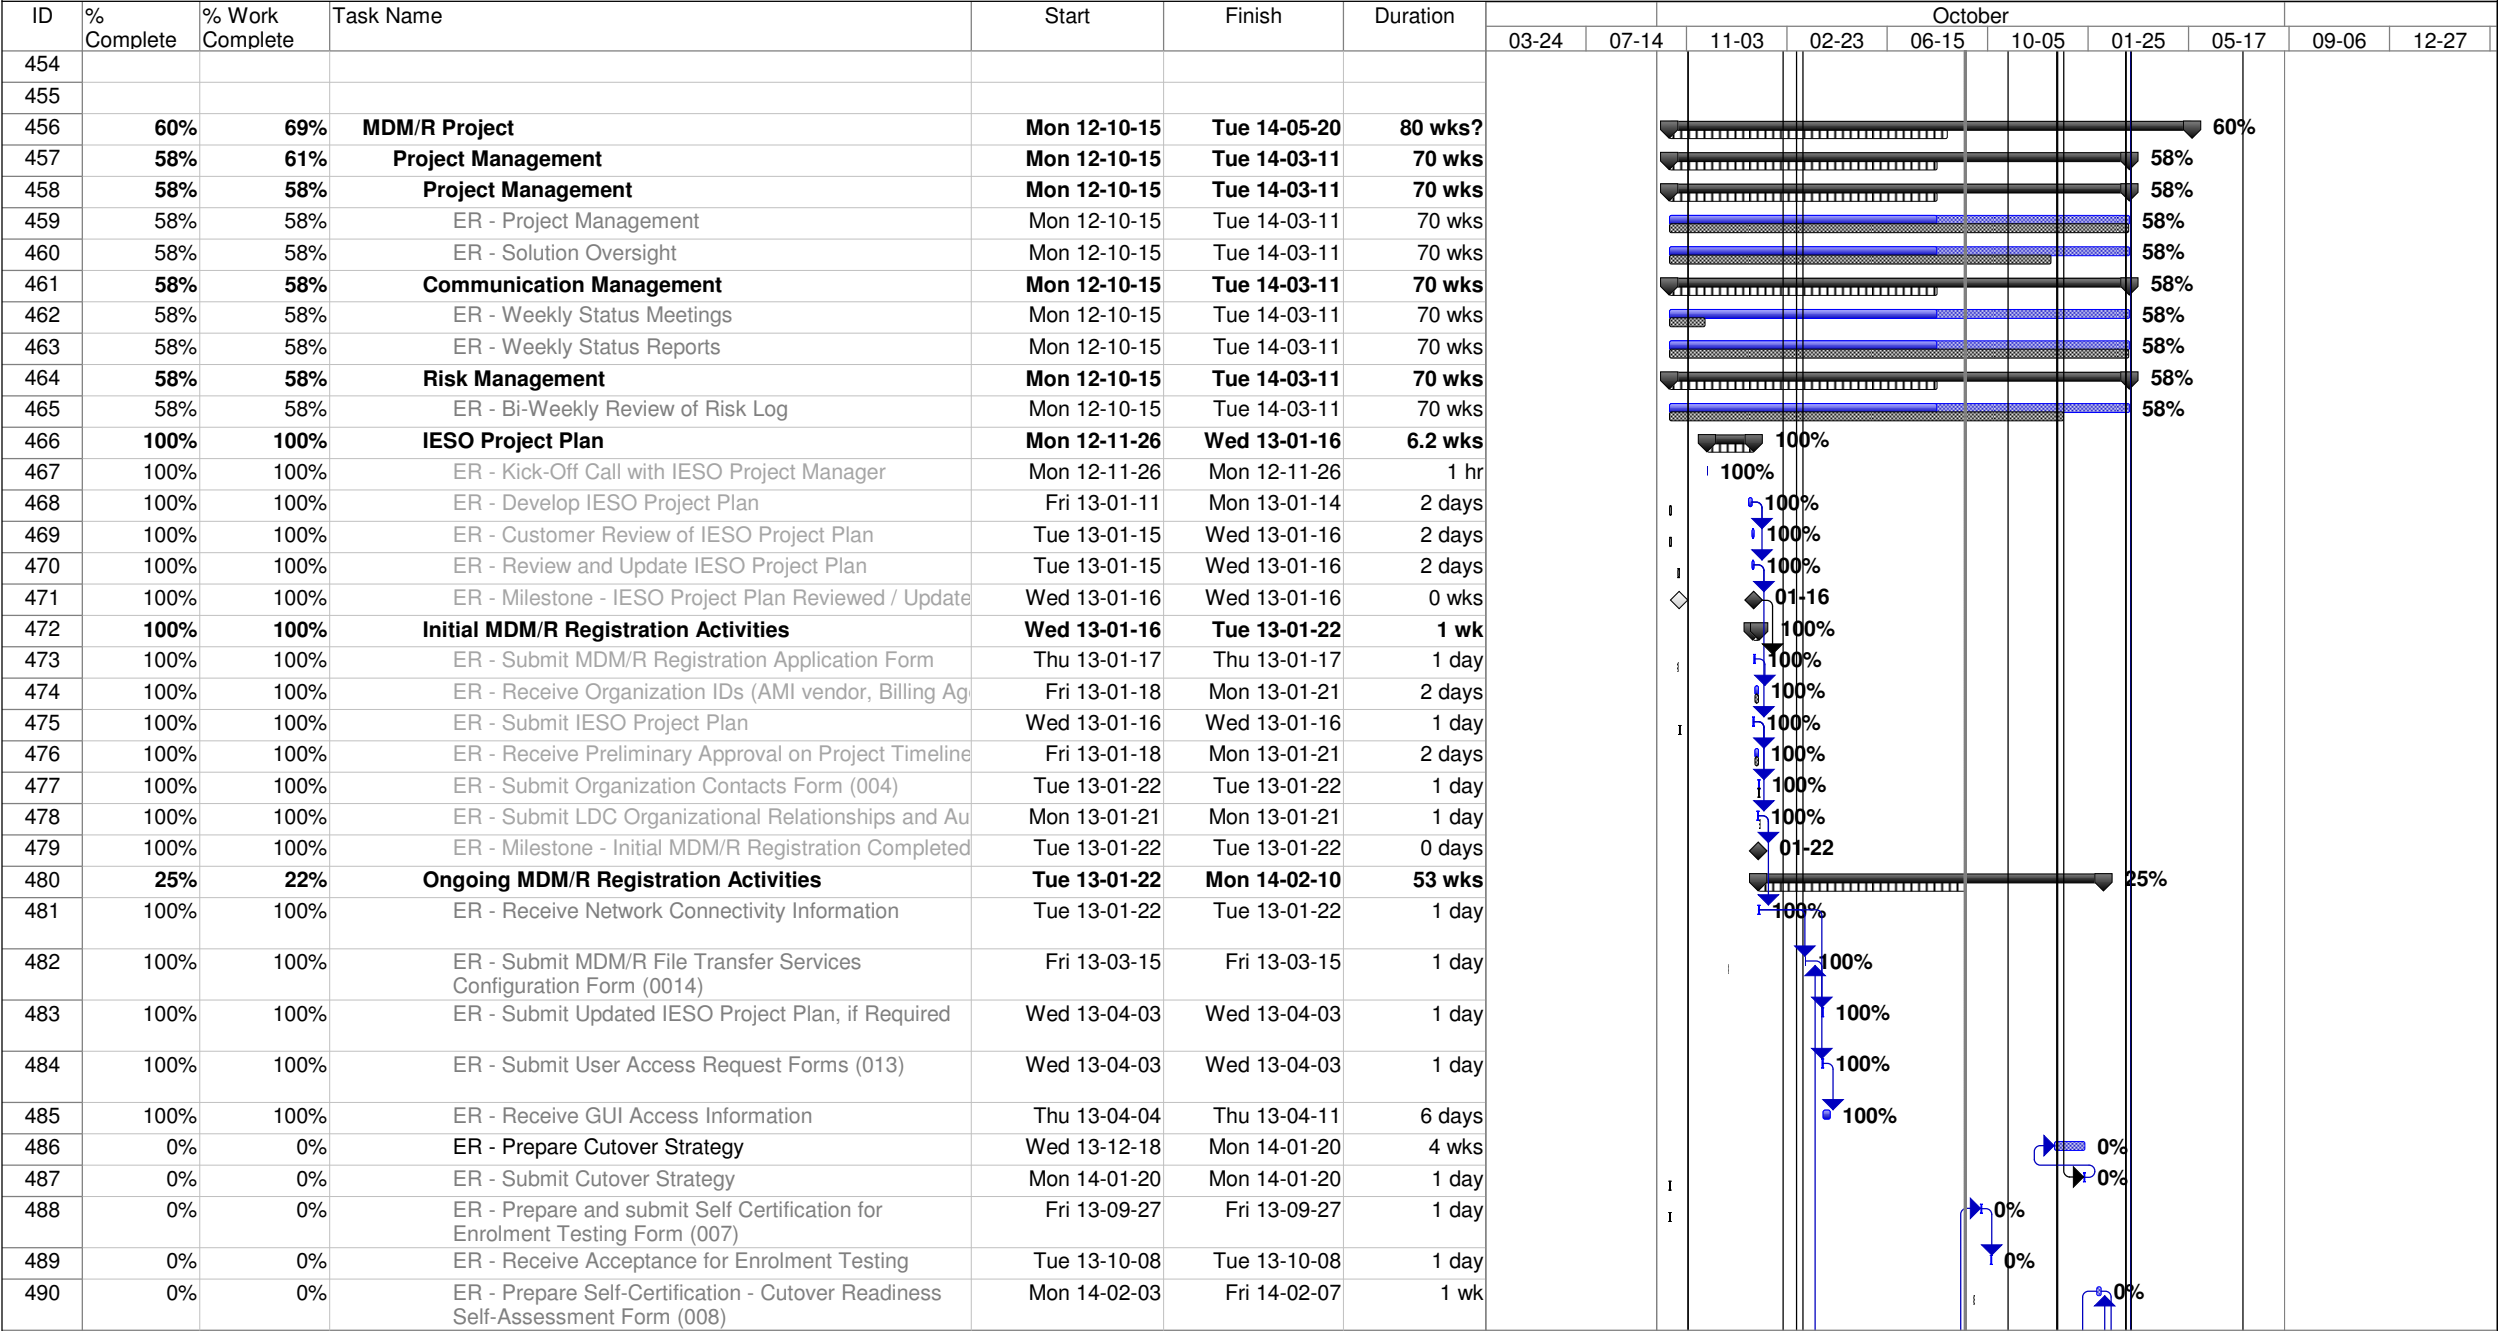


EnWin EnStar Project Plan - September 2013

ID	% Complete	% Work Complete	Task Name	Start	Finish	Duration	October								09-06	12-27	
							03-24	07-14	11-03	02-23	06-15	10-05	01-25	05-17			
491	0%	0%	ER - Submit Self-Certification - Cutover Readiness Self-Assessment Form (008)	Mon 14-02-10	Mon 14-02-10	1 day								0%			
492	0%	0%	ER - Receive Acceptance for Cutover Readiness	Mon 14-02-10	Mon 14-02-10	1 day								0%			
493	100%	100%	Solution Definition Phase	Mon 12-10-15	Tue 12-11-13	4.4 wks											
494	100%	100%	Project Kick-Off	Mon 12-10-15	Tue 12-10-23	1.4 wks											
495	100%	100%	ER - Prepare for Kick-Off Meeting	Mon 12-10-15	Fri 12-10-19	5 days											
496	100%	100%	ER - Project Kick-Off Meeting	Mon 12-10-22	Tue 12-10-23	2 days											
497	100%	100%	Discovery	Wed 12-10-24	Tue 12-11-13	3 wks											
498	100%	100%	ER - Prepare for Discovery Workshops	Wed 12-10-24	Fri 12-10-26	2.14 days											
499	100%	100%	ER - Hold Discovery Workshops	Fri 12-10-26	Fri 12-11-02	5 days											
500	100%	100%	ER - Analysis of Key Business Decisions at Executive	Fri 12-11-02	Fri 12-11-02	0 wks											
501	100%	100%	ER - Document Discovery Workshop Findings	Mon 12-11-12	Tue 12-11-13	2 days											
502	100%	100%	ER - Milestone - Documented Discovery Workshop Fir	Tue 12-11-13	Tue 12-11-13	0 days											
503	100%	100%	Solution Design Phase	Wed 13-01-09	Mon 13-06-10	21.4 wks											
504	100%	100%	Business Process Changes Review	Wed 13-02-13	Tue 13-03-26	5.6 wks											
505	100%	100%	ER - Draft Business Process Change Requirements	Wed 13-02-13	Wed 13-02-20	1 wk											
506	100%	100%	ER - Review Business Process Change Requirements	Thu 13-02-21	Fri 13-02-22	1 day											
507	100%	100%	ER - Review Business Process Change Requirements	Tue 13-02-26	Tue 13-03-12	2 wks											
508	100%	100%	ER - Finalize Business Process Change Document	Tue 13-03-12	Tue 13-03-19	1 wk											
509	100%	100%	ER - Sign off on Business Process Change Document	Tue 13-03-19	Tue 13-03-26	1 wk											
510	100%	100%	ER - Deliverable - MDM/R Business Process Change F	Tue 13-03-26	Tue 13-03-26	0 wks											
511	100%	100%	ER - Milestone - Business Process Changes Completed	Tue 13-03-26	Tue 13-03-26	0 days											
512	100%	100%	CIS Design Document	Tue 13-03-26	Fri 13-03-29	0.6 wks											
513	100%	100%	ER - Deliver Plan to Execute CIS Modifications	Tue 13-03-26	Fri 13-03-29	3 days											
514	100%	100%	Unit Test Planning	Wed 13-01-09	Wed 13-02-13	5.2 wks											
515	100%	100%	ER - Prepare Unit Test Plan	Wed 13-01-09	Fri 13-01-18	8 days											
516	100%	100%	ER - Review Unit Test Plan	Mon 13-01-21	Tue 13-01-22	2 days											
517	100%	100%	ER - Review Unit Test Plan with EnWin	Wed 13-01-23	Wed 13-01-23	1 day											
518	100%	100%	ER - EnWin Review of Test Plan Document	Wed 13-01-23	Wed 13-01-30	1 wk											
519	100%	100%	ER - Finalize Test Plan Document	Thu 13-01-31	Wed 13-02-06	1 wk											
520	100%	100%	ER - Test Plan Sign-Off	Wed 13-02-06	Wed 13-02-13	1 wk											
521	100%	100%	ER - Deliverable - Unit Test Plan Document	Wed 13-02-13	Wed 13-02-13	0 days											
522	100%	100%	Cutover Planning	Thu 13-02-07	Mon 13-03-25	6.4 wks											
523	100%	100%	ER - Meeting to Identify Cutover Strategy	Thu 13-02-07	Thu 13-02-07	1 day											
524	100%	100%	ER - Prepare Cutover Strategy	Fri 13-02-08	Thu 13-02-14	1 wk											
525	100%	100%	ER - Review Cutover Strategy	Thu 13-02-14	Fri 13-03-01	2 wks											
526	100%	100%	ER - Finalize Cutover Strategy	Mon 13-03-04	Fri 13-03-08	1 wk											
527	100%	100%	ER - Sign Off on Cutover Strategy	Mon 13-03-11	Fri 13-03-22	2 wks											
528	100%	100%	ER - Deliverable - Cutover Strategy	Mon 13-03-25	Mon 13-03-25	0 wks											
529	100%	100%	Staff Training	Mon 13-05-06	Mon 13-06-10	5 wks											

EnWin EnStar Project Plan - September 2013

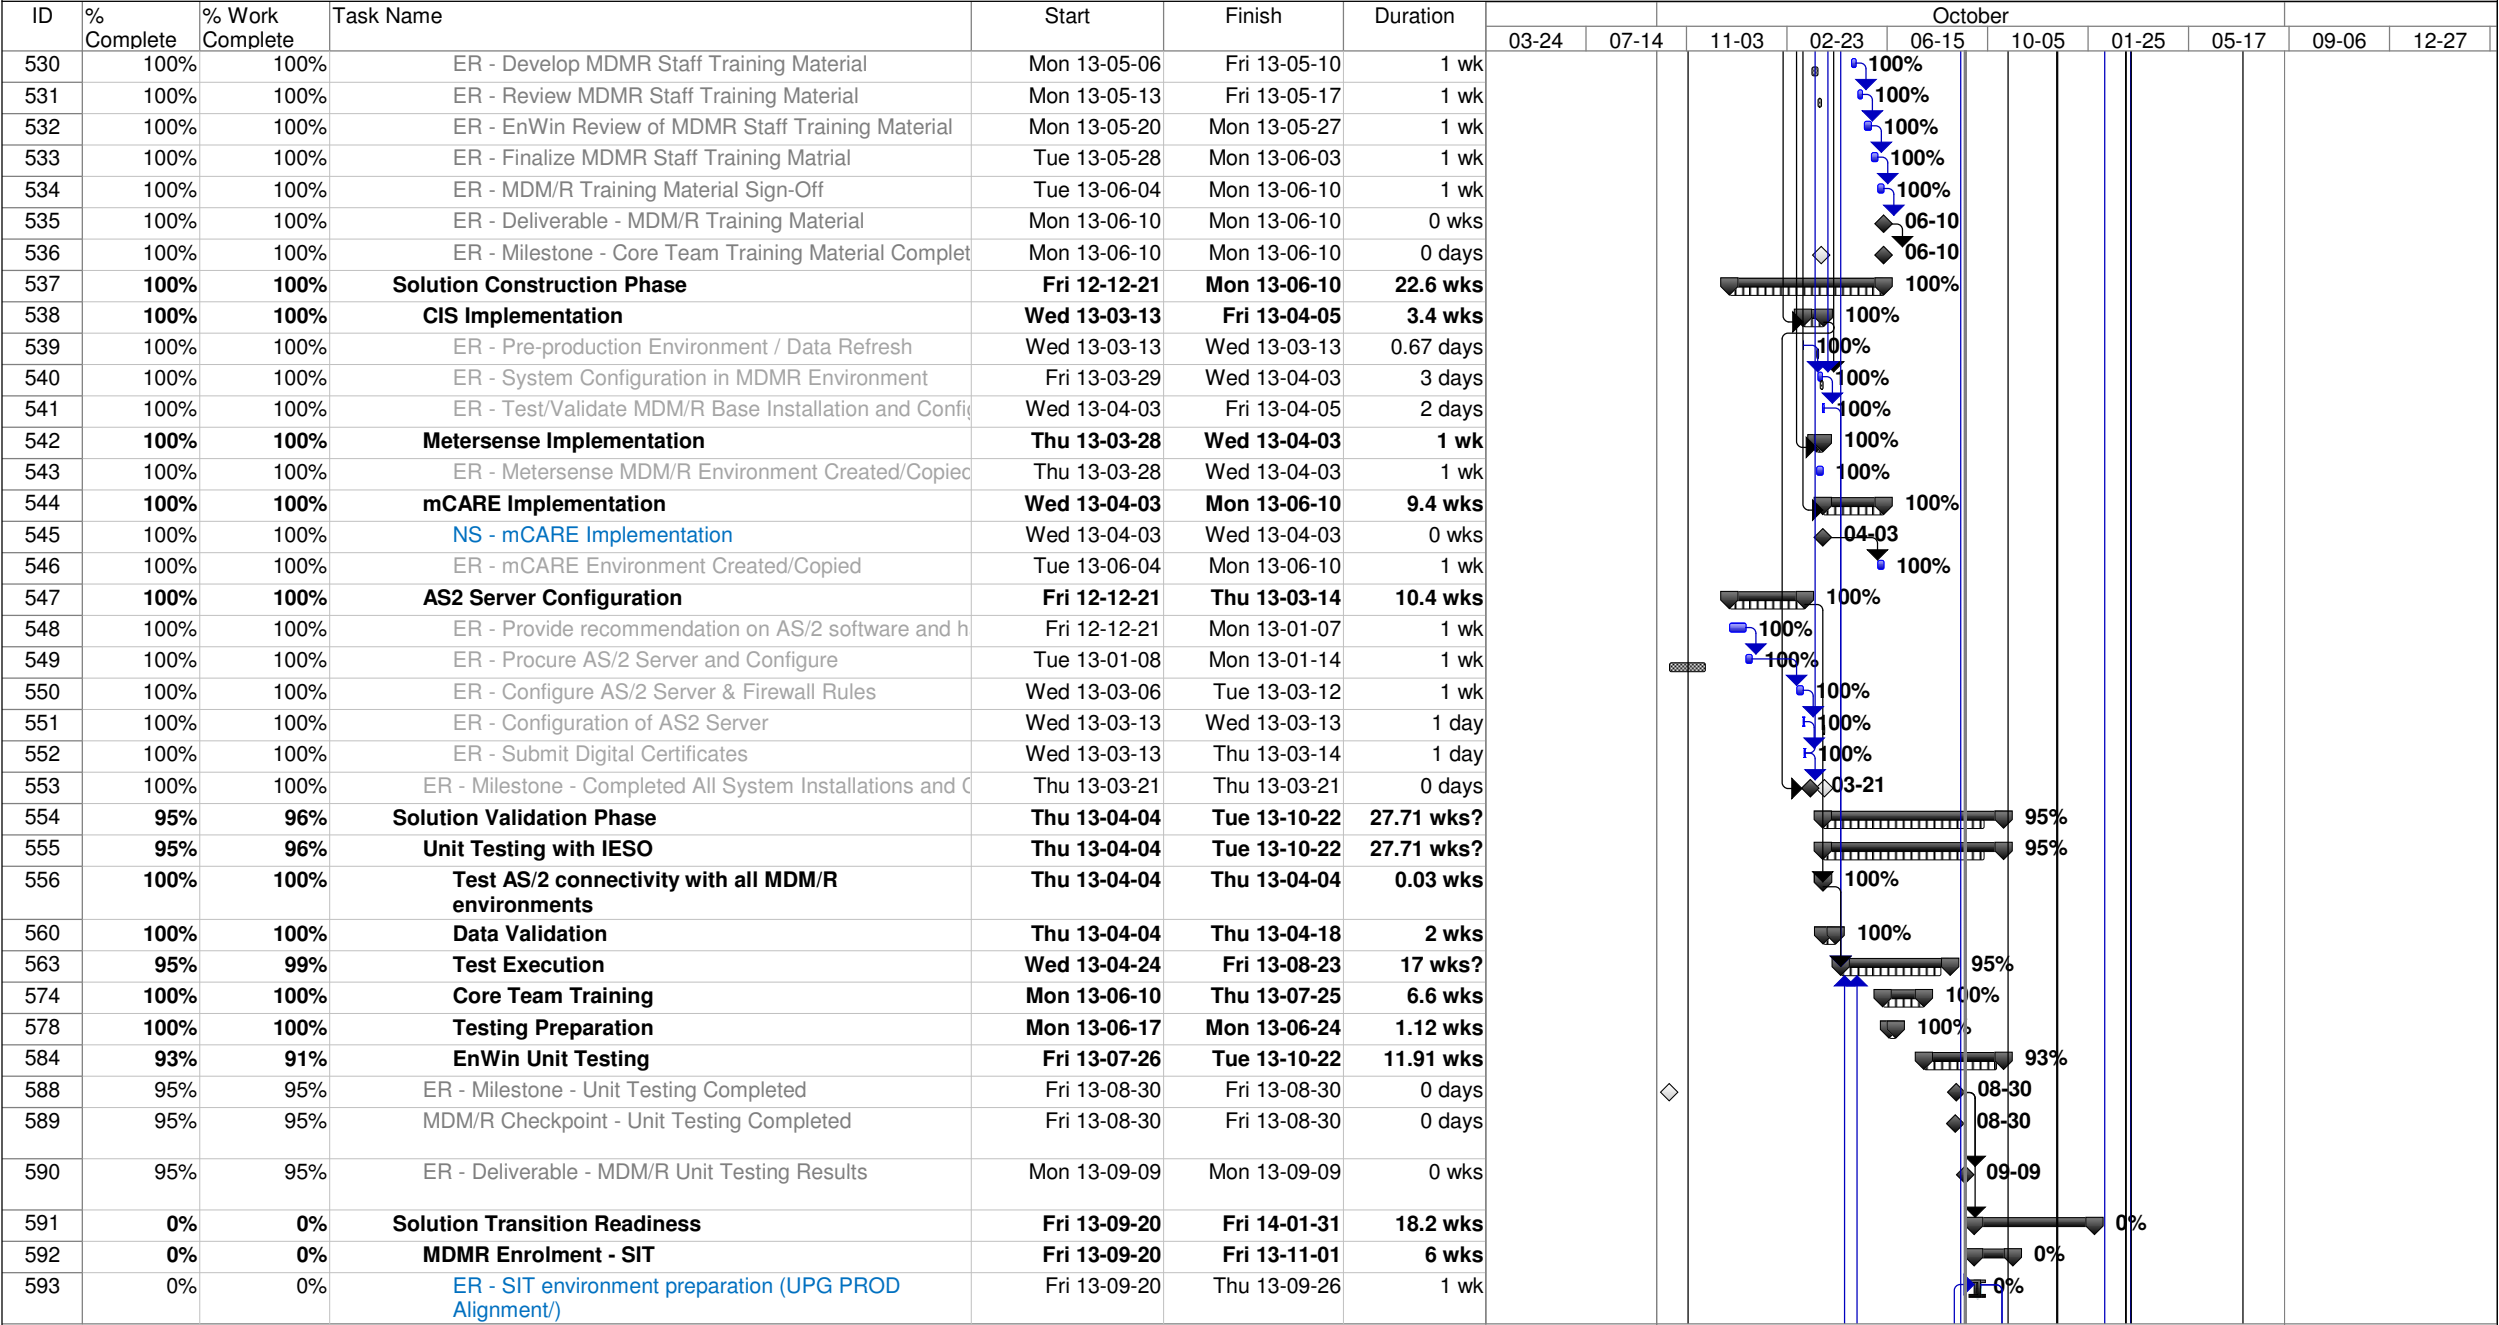

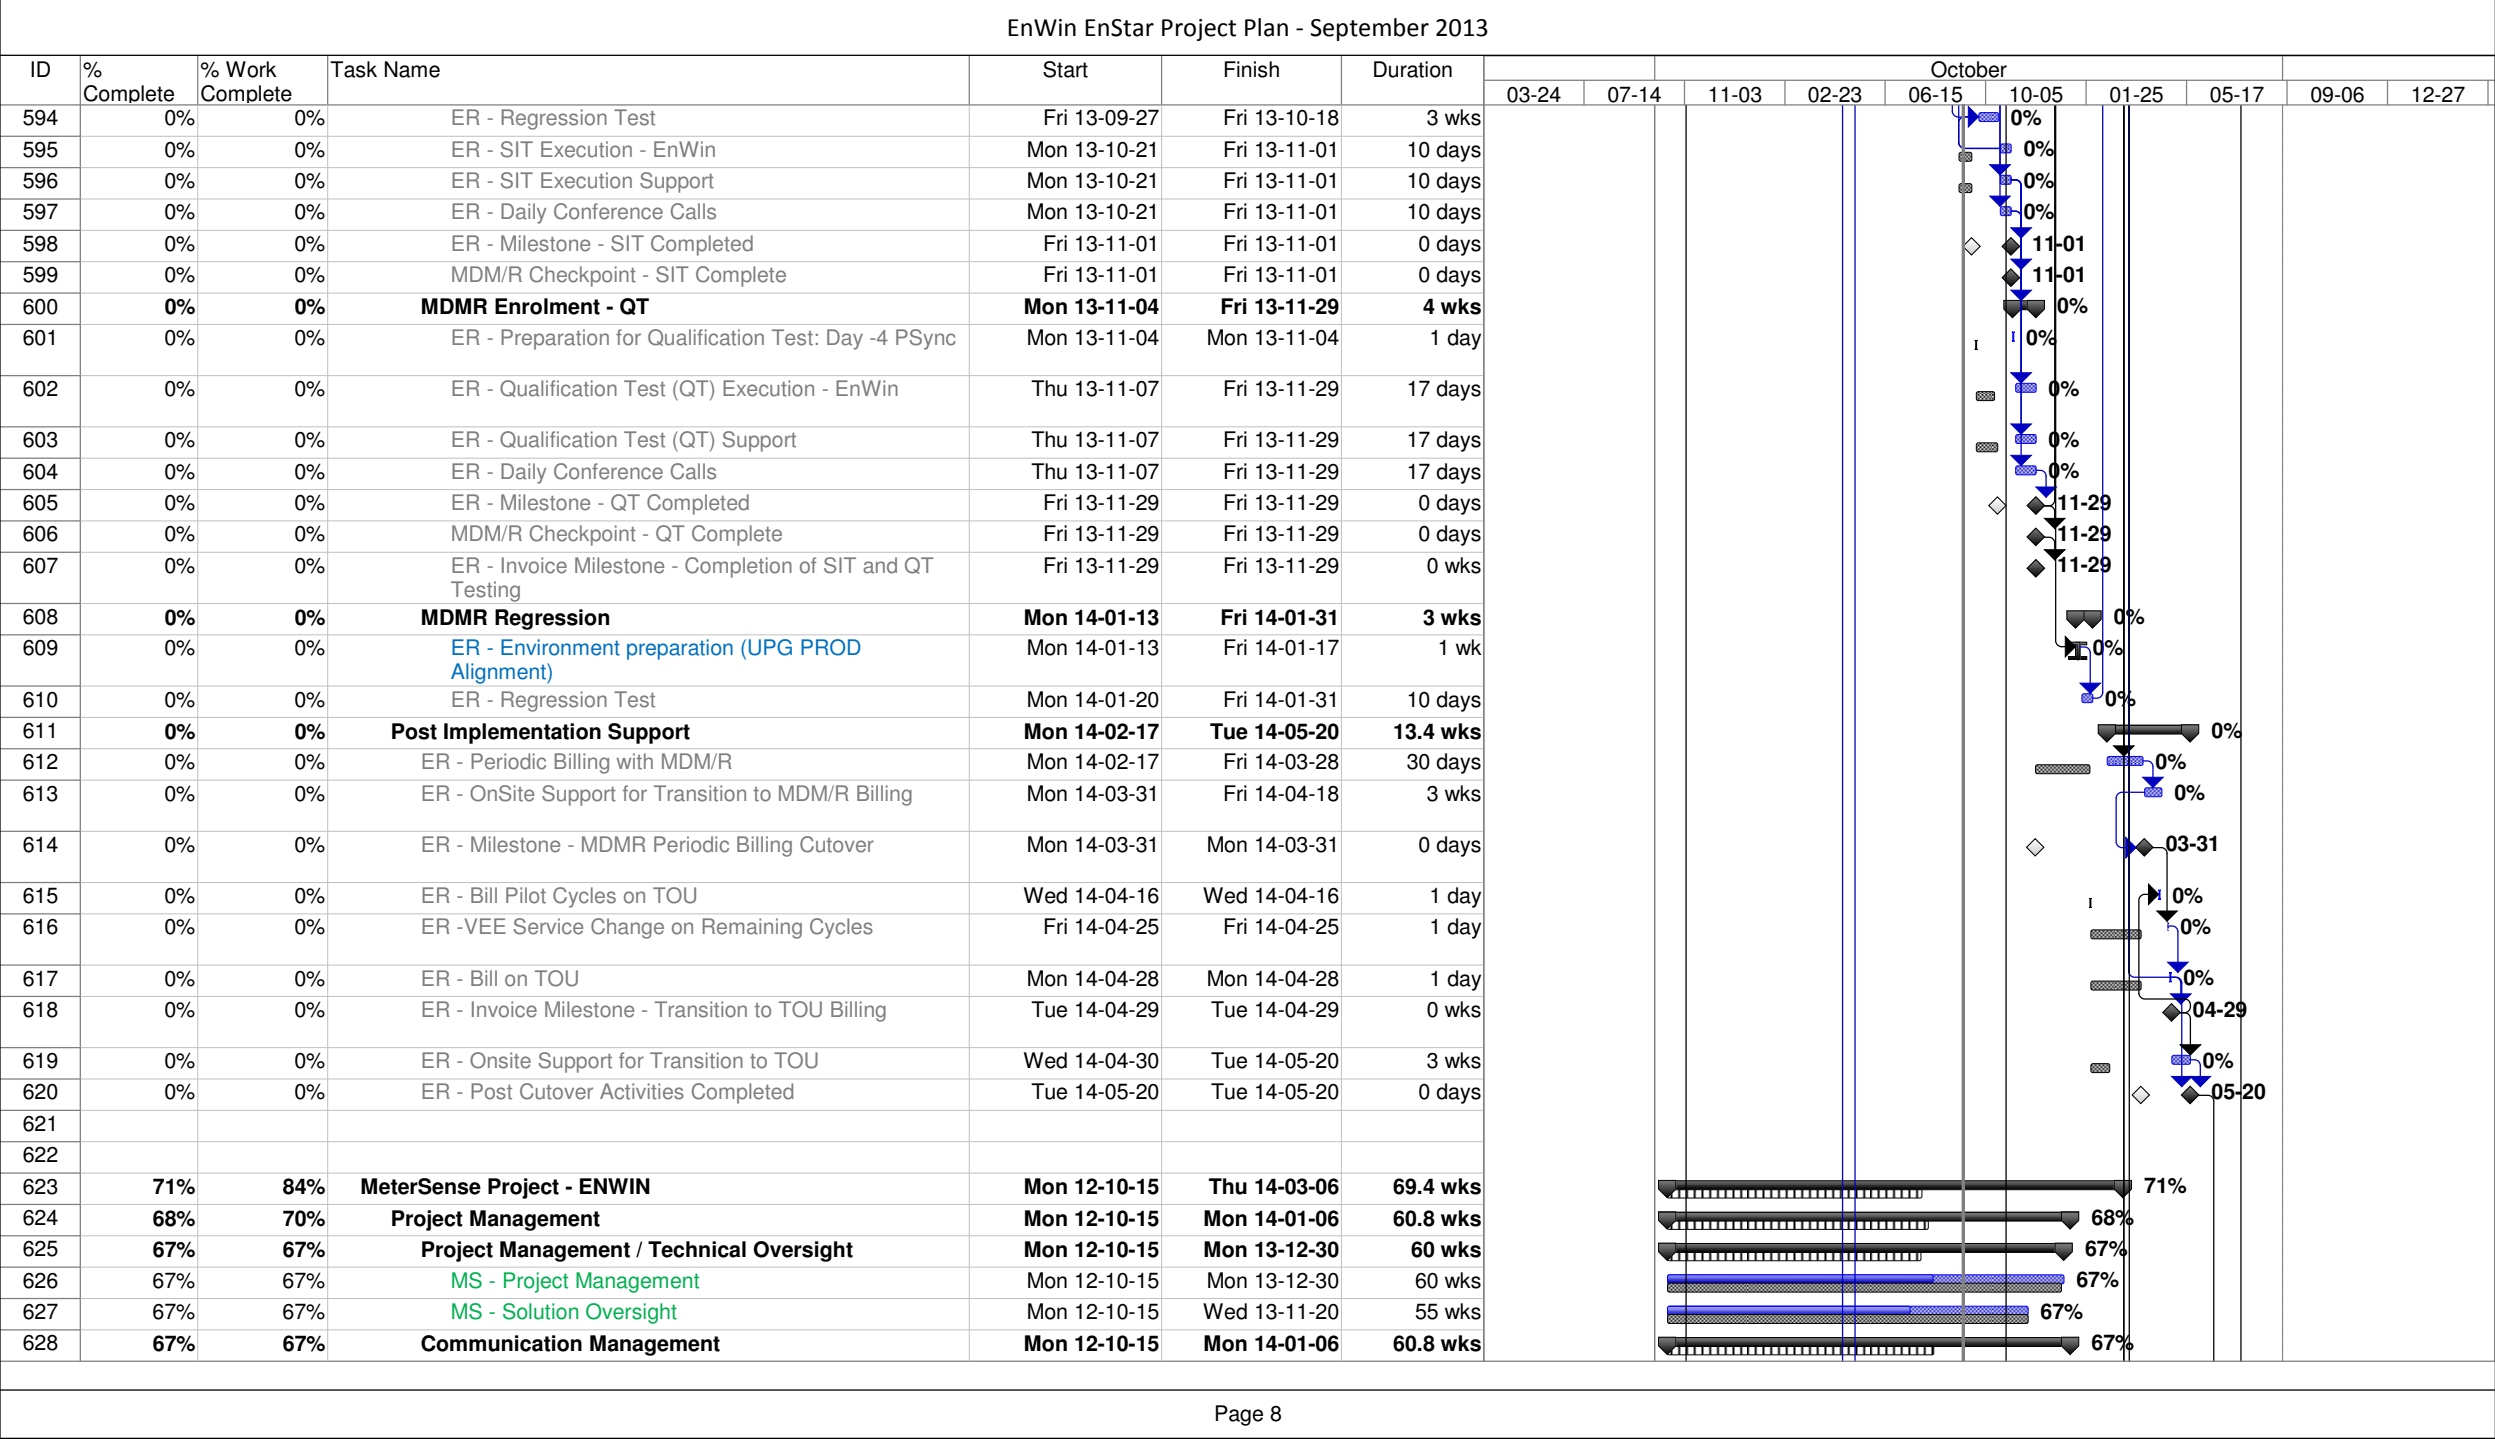

EnWin EnStar Project Plan - September 2013																
ID	% Complete	% Work Complete	Task Name	Start	Finish	Duration	October									
							03-24	07-14	11-03	02-23	06-15	10-05	01-25	05-17	09-06	12-27
629	67%	67%	MS - Weekly Status Report	Mon 12-10-15	Mon 13-12-30	60 wks										
630	67%	67%	MS - Weekly Project Management Status Meeting	Mon 12-10-15	Mon 13-12-30	60 wks										
631	67%	67%	MS - Weekly NorthStar MeterSense Status Meeting	Mon 12-10-15	Mon 13-12-30	60 wks										
632	67%	67%	MS - Weekly Customer MeterSense Status Meeting	Mon 12-10-15	Mon 14-01-06	60.8 wks										
633	67%	67%	Scope Management	Mon 12-10-15	Mon 13-12-30	60 wks										
634	67%	67%	MS - Manage Project Scope - Change Control - Impact Assessment	Mon 12-10-15	Mon 13-12-30	60 wks										
635	72%	77%	Risk Management	Mon 12-10-15	Wed 13-11-20	55 wks										
636	100%	100%	MS - Create Risk Log	Mon 12-10-15	Fri 12-10-26	2 wks										
637	71%	71%	MS - Bi-Weekly Review of Risk Log	Mon 12-10-15	Wed 13-11-20	55 wks										
638	100%	100%	Project Plan	Mon 12-10-15	Wed 13-02-20	17 wks										
639	100%	100%	MS - Initial Master Project Plan	Mon 12-10-22	Fri 12-11-16	4 wks										
640	100%	100%	MS - Review Master Project Plan	Mon 12-10-15	Fri 12-11-09	4 wks										
641	100%	100%	MS - Review and Update Master Project Plan following Definition Phase	Wed 13-01-23	Wed 13-02-20	4 wks										
642	100%	100%	MS - Milestone - Project Plan Reviewed / Updated	Wed 13-02-20	Wed 13-02-20	0 wks										
643	100%	100%	NorthStar MeterSense Solution Definition Phase	Mon 12-10-15	Tue 13-02-05	15 wks										
644	100%	100%	Project Preparation	Mon 12-10-15	Fri 12-10-19	1 wk										
645	100%	100%	MS - Gather and Review Project Documentation	Mon 12-10-15	Fri 12-10-19	5 days										
646	100%	100%	MS - Hold NorthStar internal Kick-Off Meeting	Mon 12-10-15	Fri 12-10-19	5 days										
647	100%	100%	Project Kick-Off	Mon 12-10-15	Tue 12-10-23	1.4 wks										
648	100%	100%	MS - Prepare and Schedule Project Kick-Off	Mon 12-10-15	Fri 12-10-19	1 wk										
649	100%	100%	MS - Hold Project Kick-Off	Mon 12-10-22	Tue 12-10-23	2 days										
650	100%	100%	MS - Milestone - Kick-Off Meeting Held	Tue 12-10-23	Tue 12-10-23	0 wks										
651	100%	100%	NorthStar MeterSense Product Orientation Session - Training	Wed 12-10-24	Fri 12-11-02	1.6 wks										
652	100%	100%	MS - Schedule MeterSense Product Orientation Session	Wed 12-10-24	Thu 12-10-25	2 days										
653	100%	100%	MS - Prepare MeterSense Product Orientation Training Session	Fri 12-10-26	Thu 12-11-01	1 wk										
654	100%	100%	MS - Hold MeterSense Product Orientation Session	Fri 12-11-02	Fri 12-11-02	1 day										
655	100%	100%	Discovery	Wed 12-10-24	Wed 12-11-07	2.2 wks										
656	100%	100%	MS - Customer Questionnaire Completion	Mon 12-10-29	Fri 12-11-02	1 wk										
657	100%	100%	MS - Gather and Review Customer Information	Wed 12-10-24	Fri 12-10-26	3 days										
658	100%	100%	MS - Hold Discovery Workshops	Mon 12-10-29	Wed 12-10-31	3 days										
Page 9																

[illegible]

EnWin EnStar Project Plan - September 2013																
ID	% Complete	% Work Complete	Task Name	Start	Finish	Duration	October									
							03-24	07-14	11-03	02-23	06-15	10-05	01-25	05-17	09-06	12-27
715	100%	100%	MS - Data Archiving Testing	Wed 13-03-13	Tue 13-03-26	2 wks				100%						
716	100%	100%	MS - IESO Configuration	Wed 13-02-27	Tue 13-03-26	4 wks				100%						
717	100%	100%	MS - Service Order Integration Development	Tue 13-02-05	Tue 13-02-26	3 wks				100%						
718	100%	100%	MS - Service Order Integration Testing	Wed 13-02-27	Tue 13-03-26	4 wks				100%						
719	100%	100%	MS - MV 90 Development	Tue 13-02-12	Tue 13-03-12	4 wks				100%						
720	100%	100%	MS - MV 90 Testing	Wed 13-03-13	Tue 13-03-26	2 wks				100%						
721	100%	100%	MS - Transformer Loading	Tue 13-02-12	Tue 13-03-12	4 wks				100%						
722	100%	100%	MS - Transformer Loading Testing	Wed 13-03-13	Tue 13-03-26	2 wks				100%						
723	100%	100%	Milestone - Solution Feature Complete	Tue 13-03-26	Tue 13-03-26	0 wks				100%						
724	100%	100%	User Acceptance Testing Detailed Plan Document	Wed 13-03-27	Tue 13-04-30	5 wks				100%						
725	100%	100%	MS - Draft User Acceptance Testing Detailed Plan Document	Wed 13-03-27	Tue 13-04-02	1 wk				100%						
726	100%	100%	MS - Review User Acceptance Testing Detailed Plan Document	Wed 13-04-03	Tue 13-04-16	2 wks				100%						
727	100%	100%	MS - Finalize User Acceptance Testing Detailed Plan Document	Wed 13-04-17	Tue 13-04-23	1 wk				100%						
728	100%	100%	MS - User Acceptance Testing Detailed Plan Document Sign-Off	Wed 13-04-24	Tue 13-04-30	1 wk				100%						
729	100%	100%	MS - Invoice Milestone - User Acceptance Testing Detailed Plan Document	Tue 13-04-30	Tue 13-04-30	0 wks				04-30						
730	100%	100%	Training Detailed Schedule	Thu 13-02-28	Wed 13-03-27	4 wks				100%						
731	100%	100%	MS - Draft Training Detailed Schedule	Thu 13-02-28	Wed 13-03-13	2 wks				100%						
732	100%	100%	MS - Review Training Detailed Schedule	Thu 13-03-14	Wed 13-03-20	1 wk				100%						
733	100%	100%	MS - Finalize Training Detailed Schedule	Thu 13-03-21	Wed 13-03-27	1 wk				100%						
734	59%	96%	MeterSense Solution Validation Phase	Wed 13-02-27	Tue 13-10-01	30.2 wks					59%					
735	100%	100%	Testing Environment	Wed 13-02-27	Tue 13-03-26	4 wks				100%						
736	100%	100%	MS - Set-Up Testing Environment	Wed 13-02-27	Tue 13-03-26	4 wks				100%						
737	100%	100%	Functional Testing	Wed 13-03-27	Tue 13-04-16	3 wks				100%						
738	100%	100%	MS - Perform Functional Testing	Wed 13-03-27	Tue 13-04-16	3 wks				100%						
739	100%	100%	MS - Issue and Configuration Resolution	Wed 13-03-27	Tue 13-04-16	3 wks				100%						
740	100%	100%	MS - Publish Functional Testing Results	Wed 13-03-27	Tue 13-04-16	3 wks				100%						
741	100%	100%	Integration Testing	Wed 13-04-17	Tue 13-04-30	2 wks				100%						
742	100%	100%	MS - Perform Integration Testing	Wed 13-04-17	Tue 13-04-30	2 wks				100%						
743	100%	100%	MS - Issue and Configuration Resolution	Wed 13-04-17	Tue 13-04-30	2 wks				100%						
744	100%	100%	MS - Publish Integration Testing Results	Wed 13-04-17	Tue 13-04-30	2 wks				100%						
745	100%	100%	MS - Deliverable - MeterSense Test Results	Tue 13-04-30	Tue 13-04-30	0 wks				04-30						
746	81%	80%	Training	Mon 13-04-22	Tue 13-10-01	22.6 wks					81%					
747	81%	80%	Functional and Rule Engine Training	Mon 13-04-22	Tue 13-10-01	22.6 wks					81%					
754	25%	98%	User Acceptance Testing	Mon 13-05-06	Thu 13-09-26	20 wks					25%					

EnWin EnStar Project Plan - September 2013

ID	% Complete	% Work Complete	Task Name	Start	Finish	Duration			October									
							03-24	07-14	11-03	02-23	06-15	10-05	01-25	05-17	09-06	12-27		
755	98%	98%	MS - Perform User Acceptance Testing	Mon 13-05-06	Fri 13-05-17	2 wks				98%								
756	98%	98%	MS - Support Customer during User Acceptance Testing	Mon 13-05-06	Fri 13-05-17	2 wks				98%								
757	98%	98%	MS - Issue and Configuration Resolution	Mon 13-05-06	Fri 13-05-17	2 wks				98%								
758	0%	50%	MS - Invoice Milestone - Accepted Solution	Fri 13-05-17	Thu 13-09-26	18 wks				0%								
759	0%	0%	MS - Deliverable - Accepted Solution	Tue 13-10-01	Tue 13-10-01	0 wks				0%								
760	4%	15%	1.5 Years of Historical Data Loading	Mon 13-08-26	Thu 14-01-30	21.6 wks				4%								
761	25%	25%	MS - Finalize Timing of Data Load	Mon 13-08-26	Fri 13-09-13	14 days				25%								
762	0%	0%	MS - Schedule and execute data archiving and restore testing	Mon 13-09-16	Fri 13-10-04	3 wks				0%								
763	0%	0%	MS - Assemble Historical Sensus and MV90 Data	Mon 13-11-18	Fri 13-12-13	4 wks				0%								
764	0%	0%	MS - Load and Validate Data	Mon 13-12-16	Thu 14-01-30	6 wks				0%								
765	50%	21%	MeterSense Solution Production Environment Phase	Fri 13-02-01	Thu 14-03-06	55 wks				50%								
766	89%	76%	Production Environment	Fri 13-02-01	Thu 14-01-30	50 wks				89%								
767	100%	100%	MS - Procure and configure Production Server	Fri 13-02-01	Thu 13-02-14	2 wks				100%								
768	100%	100%	MS - Setup Production Environment	Fri 13-02-15	Fri 13-03-15	4 wks				100%								
769	100%	100%	MS - Regression Testing of Solution from Upgrade to RNI 3.1	Mon 13-03-04	Fri 13-03-15	2 wks				100%								
770	0%	0%	MS - Confirm Production Environment Readiness	Fri 14-01-24	Thu 14-01-30	1 wk				0%								
771	0%	0%	MS - MeterSense Soft Go-Live	Thu 14-01-30	Thu 14-01-30	0 wks				0%								
772	0%	0%	Business Process Training (prior to Live)	Tue 13-11-19	Mon 14-02-03	10.2 wks				0%								
773	0%	0%	MS - Prepare Business Process Training	Tue 13-11-19	Mon 13-12-02	2 wks				0%								
774	0%	0%	MS - Hold Business Process Training (Core Team)	Tue 13-12-03	Mon 13-12-09	1 wk				0%								
775	0%	0%	MS - Hold Business Process Training (Engg. Team)	Mon 14-02-03	Mon 14-02-03	1 day				0%								
776	0%	0%	MS - Milestone - Business Process Training Complete	Mon 14-02-03	Mon 14-02-03	0 wks				0%								
777	0%	0%	Production Environment Release	Mon 14-02-10	Thu 14-02-20	1.8 wks				0%								
778	0%	0%	MS - Perform Cut-Over Activities	Mon 14-02-10	Fri 14-02-14	1 wk				0%								
779	0%	0%	MS - Release Production Environment to End Customer Base	Mon 14-02-17	Mon 14-02-17	0.1 wks				0%								
780	0%	0%	MS - Validate Success (Test Cases Sub-Set)	Mon 14-02-17	Thu 14-02-20	0.7 wks				0%								
781	0%	0%	MS - Invoice Milestone - Solution Live	Thu 14-02-20	Thu 14-02-20	0 wks				0%								
782	0%	0%	Post-Production Environment - Enhanced Support	Fri 14-02-21	Thu 14-03-06	2 wks				0%								
783	0%	0%	MS - Support and Consult - as required	Fri 14-02-21	Thu 14-03-06	2 wks				0%								
784	0%	0%	MS - Milestone - MeterSense Project Completed	Thu 14-03-06	Thu 14-03-06	0 wks				0%								
785	0%	0%	Milestone - Final Acceptance of Project Closeout	Wed 14-06-25	Wed 14-06-25	0 wks				0%								
