

August 21, 2015

Ms. Pascale Duguay
Facilities Applications
Ontario Energy Board
2300 Yonge Street, Suite 2700
Toronto, Ontario
M4P 1E4

Dear Ms. Duguay:

**Re: Union Gas Limited (“Union”)
Panhandle 2015 Replacement Project
Board File # EB-2015-0041**

Please find attached three Requests to Vary for the above-noted project.

Union believes that these changes are not significant and would appreciate your timely review and approval of these requests, as construction is scheduled to start August 28, 2015.

In the event that you have any questions or would like to discuss in more detail, please do not hesitate to contact me at 519-436-5457.

Sincerely,

W. T. (Bill) Wachsmuth, RPF
Senior Administrator, Regulatory Projects

cc: Zora Crnojacki, OEB Project Advisor

REQUEST TO VARY

Project Name: Panhandle 2015 Replacement Project

OEB File Number: EB-2015-0041

Request to Vary: 1

Description and Rationale for Change

Union is proposing changing the construction technique for the crossings of Patillo Road and Wallace Line. Union's original proposal had been to open cut these road crossings. Union is now proposing to complete these crossings using a directional drill. Union has had requests from the local Municipality and adjacent landowner to complete these crossings using directional drills. Drilling the roads will reduce the impacts to local residents.

Construction and Restoration Practices

Union will follow its standard practice for directional drilled crossings to complete the work.

Environmental

No new environmental mitigation measures will be required.

Consultation

Union has met with all of the directly affected landowners and the Municipality of Lakeshore and no concerns have been identified.

Lands

No additional land rights are required.

Costs

These changes will not result in any change to the total cost of the project.

Schedule

This change will not result in a change to the in-service date of the project.



Attachments

A map showing the location of Patillo Road and Wallace line is attached at Schedule 1.

Union Gas Limited Proposed NPS 16 Panhandle Replacement Route

EB-2015-0041
Request to Vary 1
Schedule 1

LEGEND:
----- 2015 NPS16 Panhandle Replacement

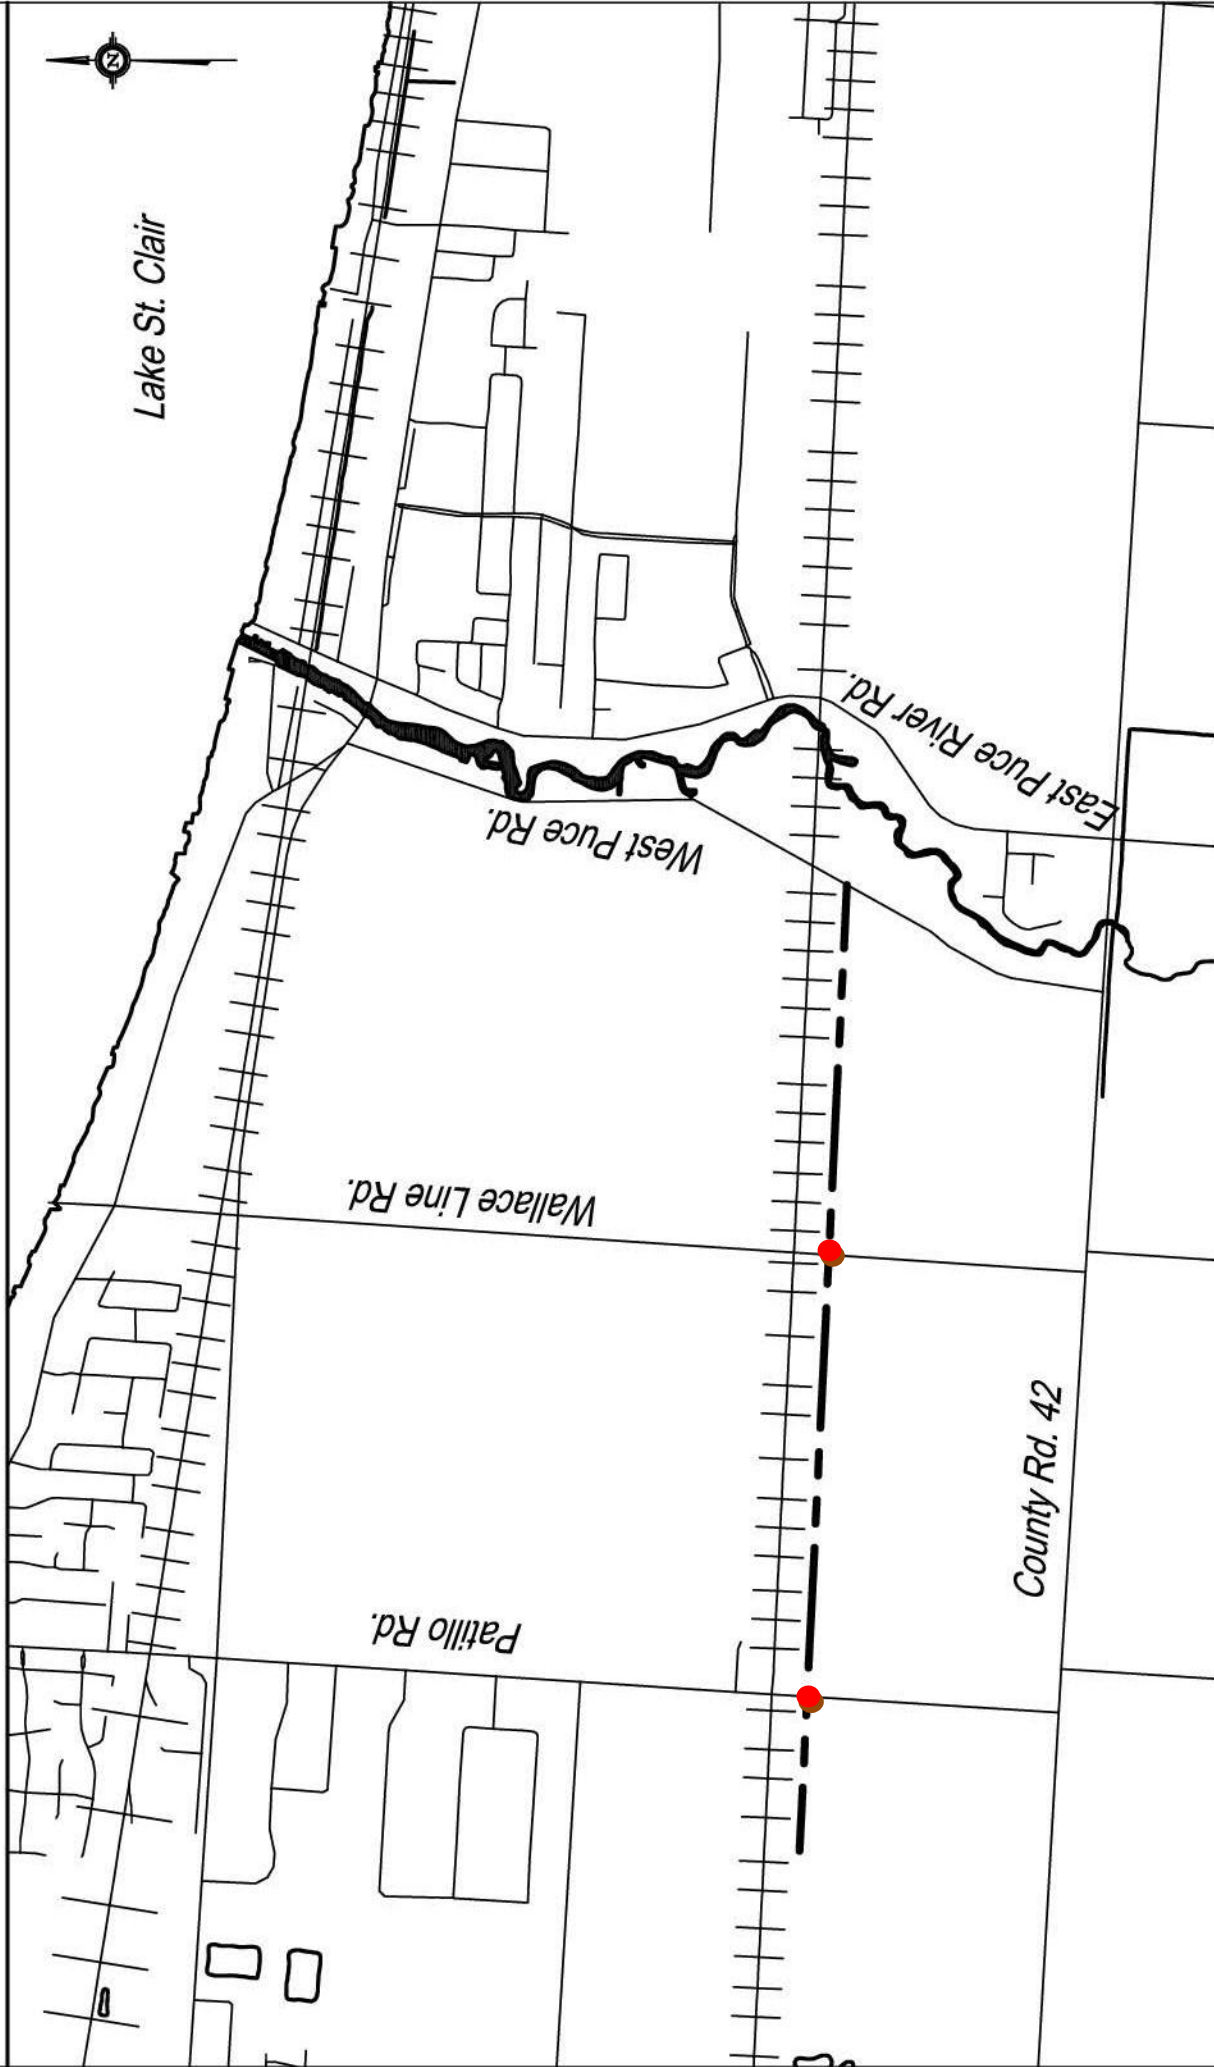

REQUEST TO VARY

Project Name: Panhandle 2015 Replacement Project

OEB File Number: EB-2015-0041

Request to Vary: 2

Description and Rationale for Change

Union is proposing a change to the construction schedule for this project.

While completing the Stage 2 archaeological assessment a large scatter of mid to-late 19th century historic Euro-Canadian artifacts with a small component of early 19th century artifacts were discovered. The discovery of this number of artifacts requires Stage 3 and 4 archaeological assessments be completed.

The property where the artifacts were discovered is owned by Hydro One and administered by Infrastructure Ontario. In order for Infrastructure Ontario to provide Union with the necessary land rights to construct the pipeline Union was required to complete the archaeological assessments.

The archaeological assessment and Infrastructure Ontario's Class EA process have taken longer to complete than expected and Union does not believe that it will be able to construct the entire project in 2015.

Union is proposing to complete the section of pipeline west of Patillo Road in 2015 and return in 2016 to complete the remainder of the project.

Construction and Restoration Practices

This change will not impact any construction procedures.

Environmental

No new environmental mitigation measures will be required.

Consultation

Union has consulted with the Ministry of Tourism, Culture and Sport's regarding this site. They have reviewed the assessments that have been completed to date. They have agreed to Union proposed plans for the site. There are no landowners issues associated with this change.

Lands

No additional land rights are required.

Costs

These changes will result in a small increase in costs due to constructing occurring over two years. The final project costs will be reported in the Post Construction Financial Report.

Schedule

This work west of Patillo Road will be completed in the fall of 2015, with remainder of the project being completed in 2016.



Attachments

A map showing the location of the 2015 and 2016 construction is attached at Schedule 1.

Union Gas Limited Proposed NPS 16 Panhandle Replacement Route

EB-2015-0041
Request to Vary 2
Schedule 1

LEGEND:
----- 2015 NPS16 Panhandle Replacement

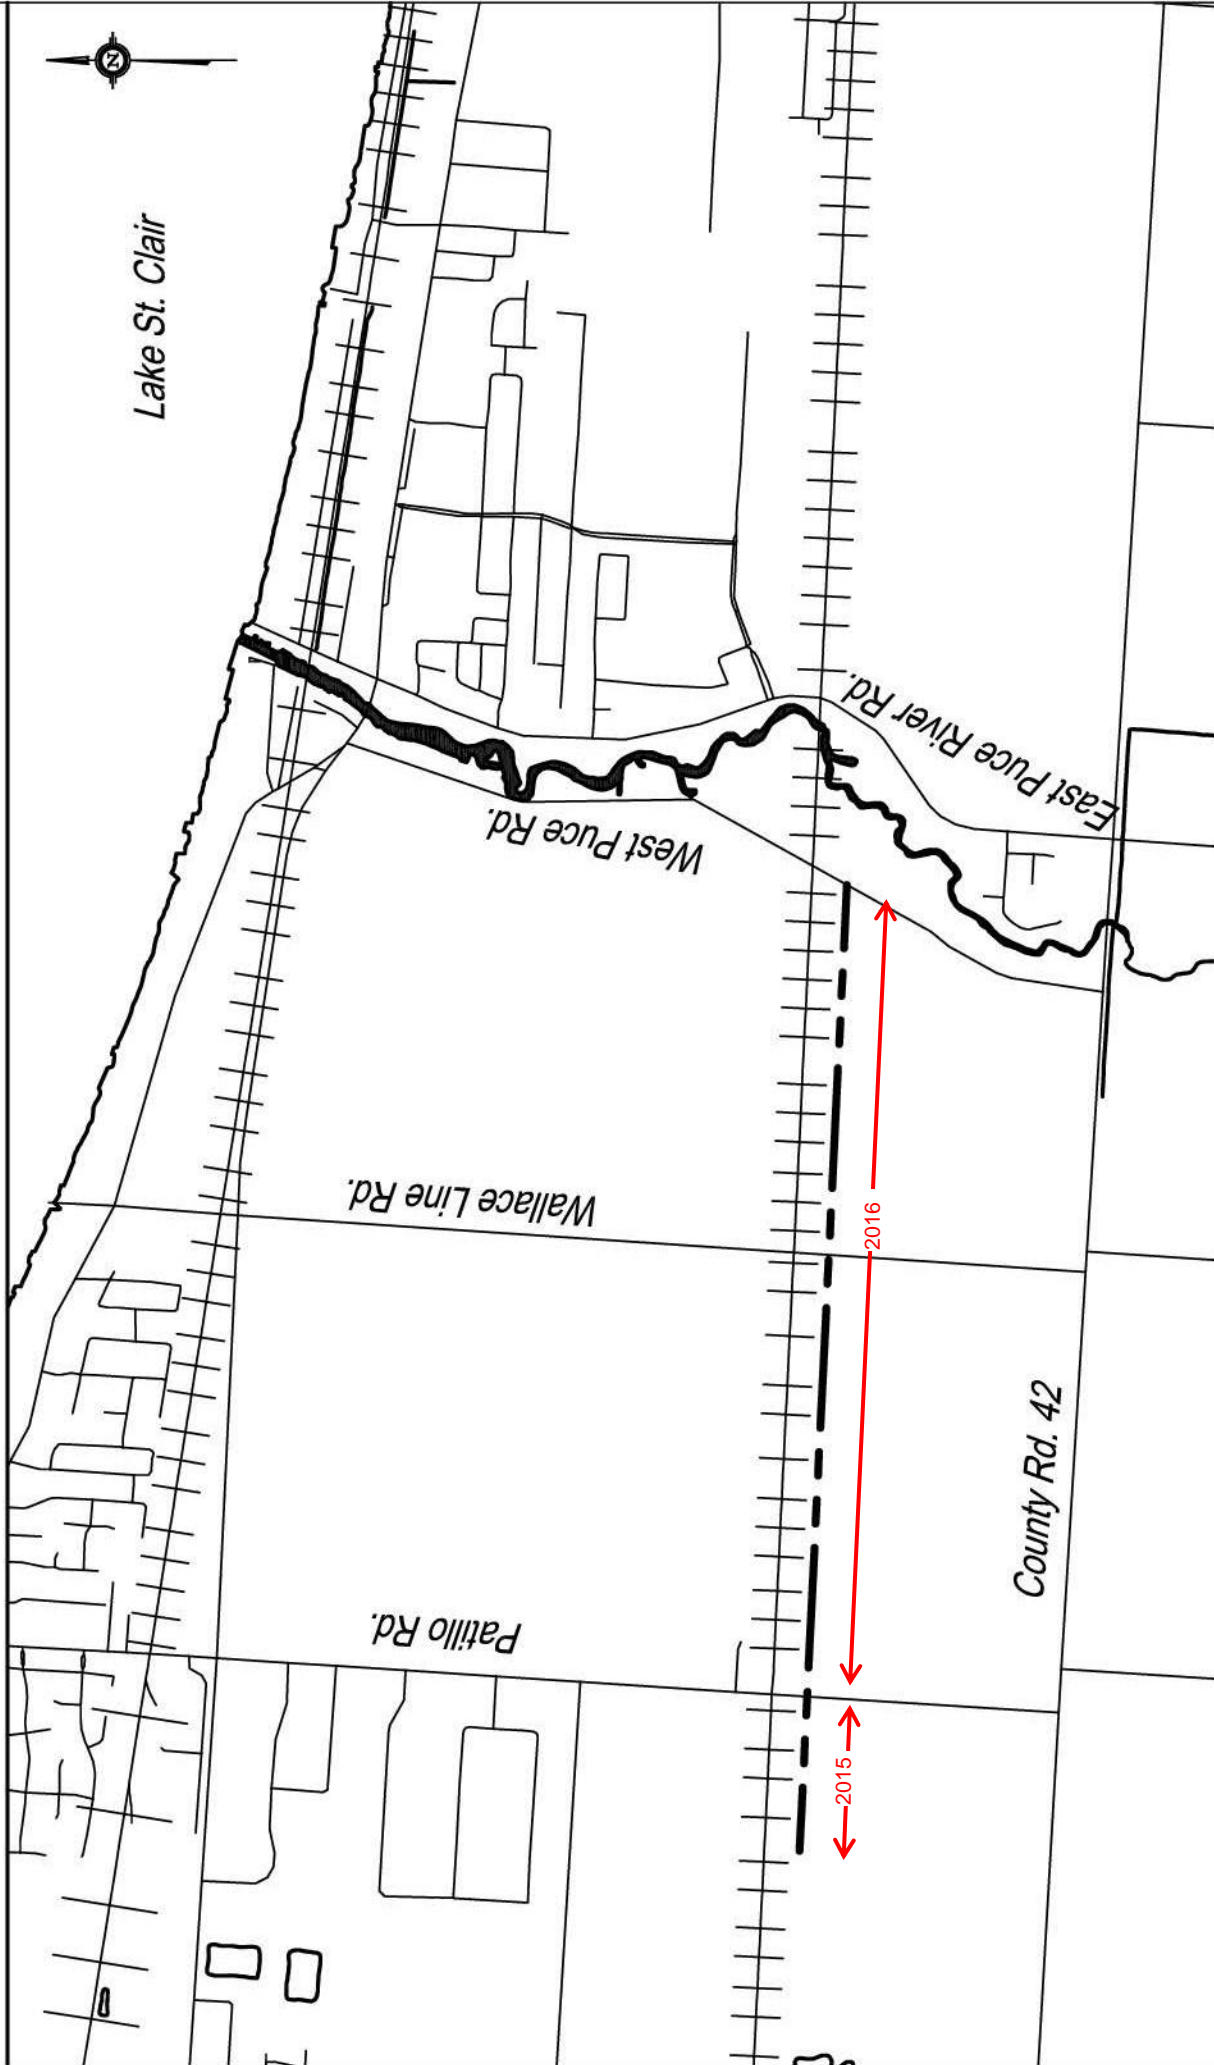

REQUEST TO VARY

Project Name: 2015 Panhandle Replacement Project

OEB File Number: EB-2015-0041

Request to Vary: 3

Description and Rationale for Change

Union is proposing changes in the vicinity of Patillo Road Station.

Union requires additional triangular 15 x 25 x 29 metre temporary land right adjacent to the Station to facilitate pipeline construction.

Construction and Restoration Practices

There are no changes proposed for construction of the proposed facilities.

Environmental

No new environmental mitigation measures will be required.

Consultation

Union has met with the directly affected landowner and no concerns have been identified.

Lands

Union has the necessary temporary land right in place.

Costs

These changes will not result in any change to the total cost of the project.

Schedule

This change will not result in a change to the in-service date of the project.

Attachments

A map showing the location of the temporary land right is attached at Schedule 1.

