



Asha Patel
Technical Manager
Regulatory Applications

tel 416-495-5642
EGIRegulatoryProceedings@enbridge.com

Enbridge Gas Inc.
500 Consumers Road
North York, Ontario M2J 1P8
Canada

October 15, 2020

VIA EMAIL and RESS

Ms. Christine E. Long
Board Secretary
Ontario Energy Board
2300 Yonge Street, 27th Floor
Toronto, ON M4P 1E4

Dear Ms. Long:

**Re: Enbridge Gas Inc. (Enbridge Gas)
Ontario Energy Board (OEB) File No.: EB-2019-0188
North Bay (Northshore and Peninsula Roads) Community Expansion Project
Change Request #3**

Please find attached Change Request #3 as submitted by Enbridge Gas Inc. ("Enbridge Gas") for the North Bay (Northshore and Peninsula Roads) Community Expansion Project ("the Project").

Enbridge Gas is filing the Request to Vary pursuant to Condition of Approval No. 5 of the OEB's EB-2019-0188 Leave to Construct Decision and Order dated May 7, 2020.

As detailed in Attachment 1, Enbridge Gas is proposing to install an additional 1.7km of pipe in 2020 due to favourable construction conditions and ideal weather. This change will not incur any additional costs outside of the project budget.

Enbridge Gas believes this change is not significant and for this reason, respectfully requests a timely review and approval of this request.

Should you have any questions concerning this submission please contact the undersigned.

Yours truly,

Asha Patel
Technical Manager, Regulatory Applications

CHANGE REQUEST

Project Name: North Bay (Northshore and Peninsula Roads) Community Expansion Project

OEB File Number: EB-2019-0188

Change Request: 3

Description and Rationale for Change

Enbridge Gas is proposing an adjustment to the scope proposed in Change Request 2. Due to favourable construction conditions and ideal weather, Enbridge Gas is proposing to install the distribution pipeline on Regal Road in 2020, totalling approximately 1.7km. The additional 1.7km on Regal Road would allow Enbridge to meet the increased customer interest on this road without impacting project costs. This change would not impact the 10-year attachment forecast and represents approximately 70% of the project scope completed in 2020 with the remaining 30% in 2021, which is unchanged from Change Request 2.

Construction and Restoration Practices

No impact to construction and/or restoration practices.

Environmental

No new environmental mitigation measures will be required.

Consultation

No additional consultation required. All stakeholders will be notified of this scope change.

Lands

No additional Land Rights or easements outside of those identified in the LTC application are required as a result of this change.

Costs

This change will not incur additional costs outside of the project budget.


Schedule


The 2020 scope of work will be in-service by November of this year. The remaining work is expected to be in-service by fall 2021.


Attachments

Attachment 1 – Change Request Form


Attachment 2 – Map showing the proposed addition to the 2020 work area

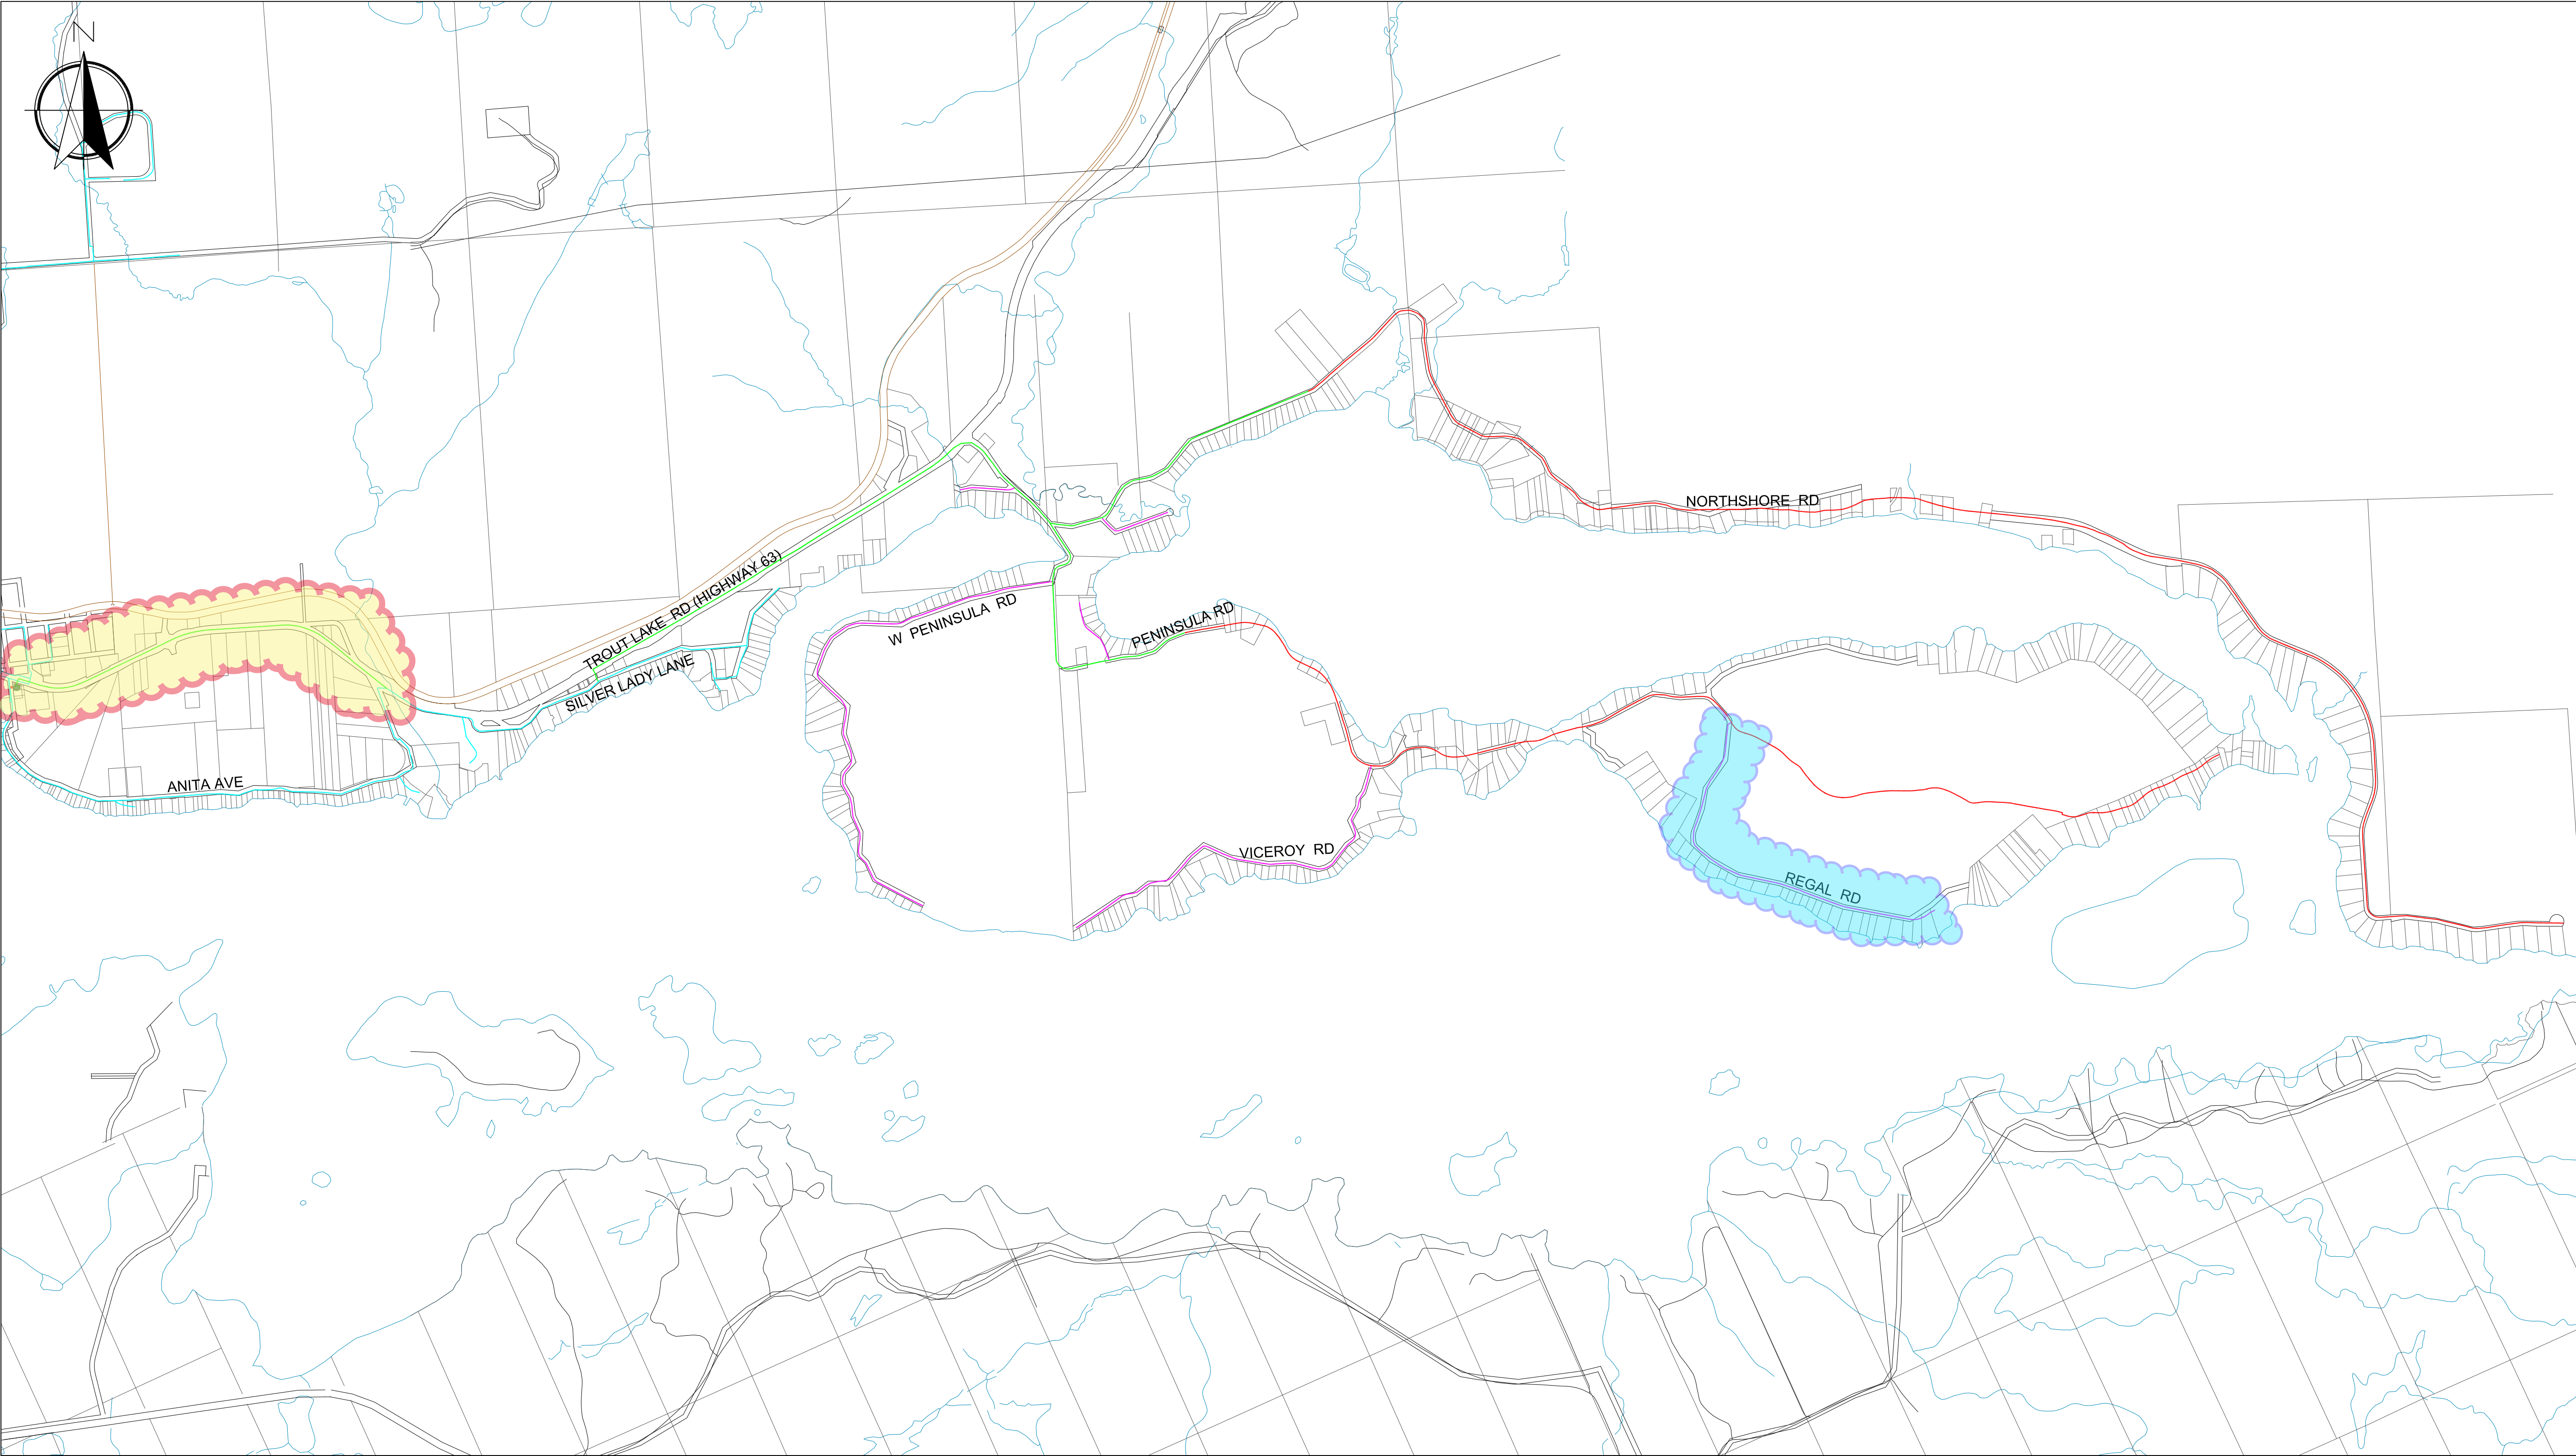



 **2020 PROJECT SCOPE**


 **ADDITION TO 2020 SCOPE**


LEGEND

 **EXISTING GAS MAIN**


 **PROPOSED 4" MAIN**

 **PROPOSED 2" MAIN**

 **PROPOSED 1 1/4" MAIN**

 **PROPOSED STATION**

SOURCE DOCUMENT INFORMATION			
Qualified Individual:		Pipeline Certificate No:	
Welder / Fuser:		Ticket Number:	
In-Service Date:		G-Tech Update By:	
Design Pressure:		Date:	
Testing	Time On:		Test Medium:
	Time Off:		Pressure:
			Pressure:
REVISIONS			
Date	By	App'd	Remarks


AS - PROPOSED

Title :
North Shore Community Expansion

Description :

INSTALL 6800m OF 4" PLASTIC GAS MAIN
INSTALL 12426m OF 2" PLASTIC GAS MAIN
INSTALL 6639m OF 1 1/4" PLASTIC GAS MAIN
INSTALL 18m OF 2" HP STEEL GAS MAIN

Project # : 76-19-300	CARS Ref # :	% SMYS :
District : NORTHEAST	Municipality : NORTH BAY	Authorized:
Drawn By : JAVANRYN	Date Drawn : 2020/03/19	Corrosion:
Scale : 1:15000	GTech # : JOBNO30705	Drawing Number 1 OF 1
