



Eric VanRuymbeke
Senior Advisor
Leave to Construct Applications
Regulatory Affairs

tel 519-436-4600 x5002241
eric.vanruymbeke@enbridge.com
EGIRegulatoryProceedings@enbridge.com

Enbridge Gas Inc.
P.O. Box 2001
50 Keil Drive North
Chatham, Ontario
N7M 5M1

VIA EMAIL and RESS

October 31, 2025

Ritchie Murray
Acting Registrar
Ontario Energy Board
2300 Yonge Street, Suite 2700
Toronto, Ontario, M4P 1E4

Dear Ritchie Murray:

**Re: Enbridge Gas Inc. (Enbridge Gas or the Company)
Ontario Energy Board (OEB) File No. EB-2022-0111
Bobcaygeon Community Expansion Project
Change Request No. 1**

Please find attached Change Request No. 1 for the Bobcaygeon Community Expansion Project (Project). Enbridge Gas is filing this Change Request pursuant to the OEB's Condition of Approval No. 5 of the OEB's Decision and Order dated May 14, 2024, granting leave to construct the Project.

As detailed within this Change Request, due to challenges with constructing approximately 490 m of Supply Lateral in shallow bedrock in the area of East Street South between Mill Street and Boyd Street, Enbridge Gas is requesting to re-route the aforementioned section of the Supply Lateral to a more constructable area along adjacent roads (Kingsway Drive, King Street, Need Street, and Boyd Street). The Project footprint has not changed as the new route is on adjacent roads where ancillary distribution pipelines were already planned as part of earlier Project scope.

As part of this Change Request, Enbridge Gas is attaching a Project Area Map identifying the revised and removed scope (Attachment 1), and a list of additional properties and the landowner (which is an existing landowner of other properties along the Supply Lateral) directly affected by the Change Request (Attachment 2). No modifications to pipeline easement or temporary land use rights are required due to this Change Request. As the Project footprint has not changed, there are no incremental impacts related to the Environmental Report and Indigenous consultation. The customer attachment forecast is also not being affected.

Enbridge Gas would like to maintain our construction schedule by commencing this change by November 17, 2025. This section of the Supply Lateral is key to maintaining our schedule to energize the entire Supply Lateral to the north portion of Bobcaygeon. This would help ensure continuous progress on the distribution construction schedules and minimize the risk of delaying customer connections this winter heating season. As such, Enbridge Gas respectfully requests approval of this Change Request as soon as possible prior to November 17.

If you have any questions, please contact the undersigned.

Sincerely,

A handwritten signature in black ink that reads "Eric VanRuyambeke". The signature is written in a cursive style with a large, prominent initial "E".

Senior Advisor, Leave to Construct Applications

c.c. Tania Persad (Enbridge Gas Counsel)
Michael Millar (OEB Counsel)
Judith Fernandes (OEB Staff)

Bobcaygeon Community Expansion Project Change Request #1

Nature and Extent of Change (including Rationale)

1. On June 14, 2023, Enbridge Gas Inc. (Enbridge Gas or the Company) filed an updated application with the Ontario Energy Board (OEB) for an order granting leave to construct approximately 34 km of Nominal Pipe Size (NPS) 6 steel coated natural gas pipeline and approximately 2 km of NPS 6 polyethylene natural gas pipeline in the City of Kawartha Lakes (including Bobcaygeon) and Township of Cavan-Monaghan (the Project). The Project is needed to supply natural gas to approximately 3,700 new customers who currently do not have access to natural gas service. The Project was selected to be eligible to receive funding assistance from Phase 2 of the Ontario Government's Natural Gas Expansion Program (NGEP). On May 14, 2024, leave to construct was granted by the OEB.
2. The scope of this Change Request is the Company's proposal to re-route approximately 490 m of NPS 6-inch high pressure polyethylene (HPPE) distribution pipeline on East Street South between Mill Street and Boyd Street to a more constructable area along Kingsway Drive, King Street, Need Street, and Boyd Street. The new route will add approximately 350 m of NPS 6 HPPE distribution pipeline to the Supply Lateral, and as a result will remove approximately 750 m of ancillary distribution pipeline from the scope of the Project. A map identifying the removed and revised scope is included at Attachment 1.

3. The purpose of this Change Request is to avoid excavating through (and installing gas main within) shallow bedrock in a location that is not proposed to provide gas services to any customers in scope of the Project. The actual extent of challenges of working through rock in this area was unforeseen and was realized when construction crews began to break rock. At the rate and conditions experienced, several weeks would be added to the construction schedule. Re-routing approximately 490 m of gas main in this area of East Street South is expected to avoid both delays to the Project schedule as well as potentially significant cost impacts (described below).

Project Need

4. This Change Request does not alter the need and rationale for Enbridge Gas's Application to supply natural gas service in the Project area.

Project Cost and Economics

5. As noted above, re-routing the Supply Lateral to avoid challenging bedrock conditions will help avoid significant increases to construction costs (which would've potentially doubled for this segment, with a magnitude of impact in the hundreds of thousands of dollars) as well as weeks of additional construction time. Relative to the LTC forecast, this Change Request is anticipated to result in a cost reduction of approximately \$77,000 for this segment, due to more favourable ground conditions. This Change Request does not impact the customer attachment forecast.

Environmental Impacts

6. All work associated with this Change Request is included within the Study Area identified in the Environmental Report¹ and therefore there are no incremental environmental impacts associated with this change. All permits, approvals and clearances related to this Change Request are in place.

Impacts on Indigenous Peoples, Municipalities and Landowners

7. In addition to the original filed landowner list for the Supply Lateral², the directly affected properties and landowner (which is an existing landowner for other properties along the Supply Lateral) as a result of this Change Request are listed at Attachment 2. The Project footprint has not changed as the new route is on adjacent roads where ancillary distribution pipelines were already planned as part of earlier Project scope, and the new Supply Lateral pipeline route remains within the City of Kawartha Lakes road allowance. As a result of constructing within the Project footprint, there are no incremental impacts to landowners. The Company will maintain its construction notification protocols. No modifications to pipeline easement and/or temporary land use rights are required as a result of this Change Request.
8. There are no anticipated impacts on Indigenous Peoples; however, Enbridge Gas will provide information on the proposed change to the Indigenous communities

¹ EB-2022-0111, Exhibit F, Tab 1, Schedule 1, Attachment 1.

² EB-2022-0111, Exhibit G, Tab 1, Schedule 1, Attachment 3.

identified by the Ministry of Energy and Mines in their September 3, 2021 Delegation Letter for the Project.³


Attachments

Attachment 1 Revised Project Route Map

Attachment 2 Landowner List – Revised Supply Lateral Scope

³ EB-2022-0111, Exhibit H, Tab 1, Schedule 1, Attachment 2.

Bobcaygeon Community Expansion Project – Change Request #1

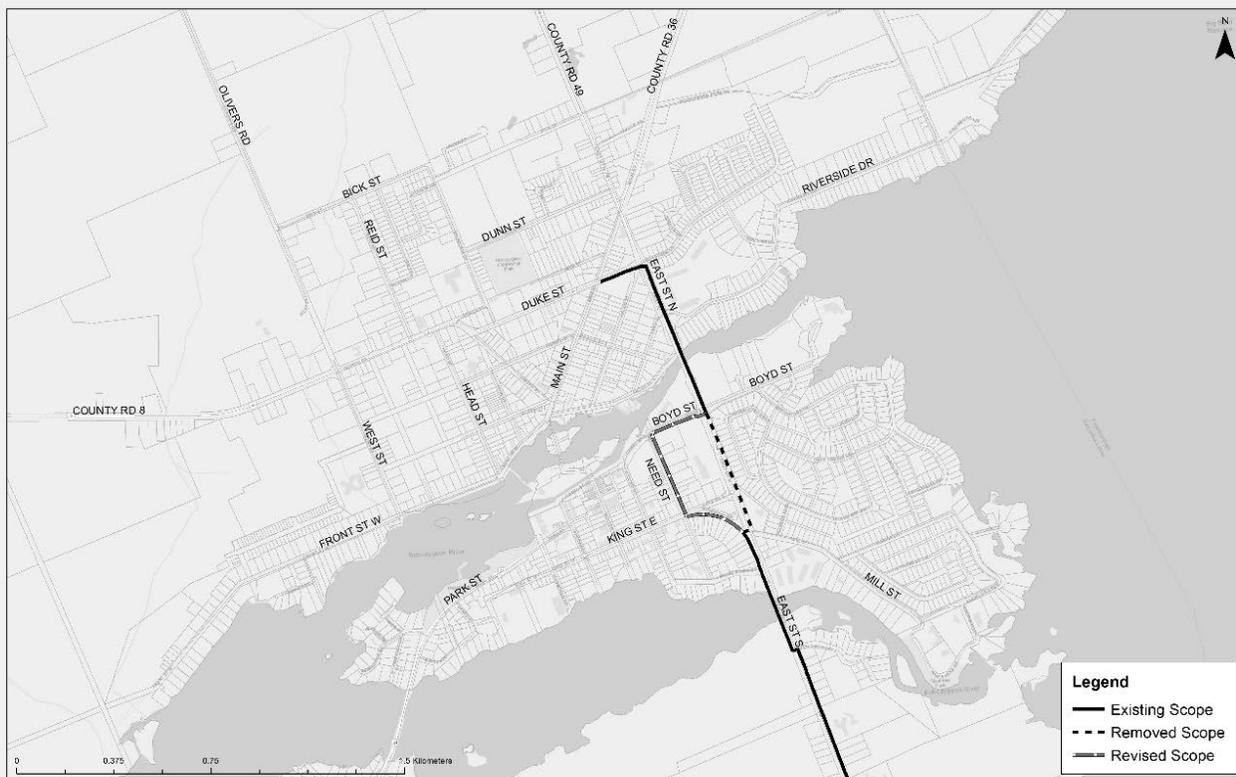

Supply Lateral - Change Request #1

Directly Affected (D) Indirectly Affected (I)	PIN	First Name	Last Name	Company Name	Address Line 1	Address Line 2	City	Province	Postal Code	Property Description	Mortgage, Lien/Lease/Encumbrances	Address Line 1	Address Line 2	City	Province	Postal Code
Directly Affected (D)	63129-0055			City of Kawartha Lakes City Hall	26 Francis Street	SNAKE POINT ROAD	Lindsay	ON	K9V 5R8	FIRSTLY: SNAKE POINT RD PL 257 SECONDLY; PT LT 15 RANGE 7 PL 11 VERULAM PT 3, 57R8191; KAWARTHA LAKES						
Directly Affected (D)	63129-0054			City of Kawartha Lakes City Hall	26 Francis Street	NEED STREET S	Lindsay	ON	K9V 5R8	NEED ST PL 70 BTN SNAKE POINT RD & KING ST; KAWARTHA LAKES						
Directly Affected (D)	63129-0056			City of Kawartha Lakes City Hall	26 Francis Street	KING STREET	Lindsay	ON	K9V 5R8	JOHN ST S PL 70 BEING KING ST; PT BLK B, C PL 11 VERULAM AS IN HWY530 & HWY908H BTN BOLTON ST & HWY 36; KAWARTHA LAKES						
Directly Affected (D)	63129-0228			City of Kawartha Lakes City Hall	26 Francis Street	NEED STREET S	Lindsay	ON	K9V 5R8	NEED ST PL 70 BTN KING ST & BOYD ST; KAWARTHA LAKES						
Directly Affected (D)	63129-0057			City of Kawartha Lakes City Hall	26 Francis Street	BOYD STREET	Lindsay	ON	K9V 5R8	PT RDAL BTN LT 15 AND LT 16 CON 10 VERULAM BEING; BOYD ST PL 70; PT BLK A PL 11 VERULAM PT 2, HWY856H; KAWARTHA LAKES						
